
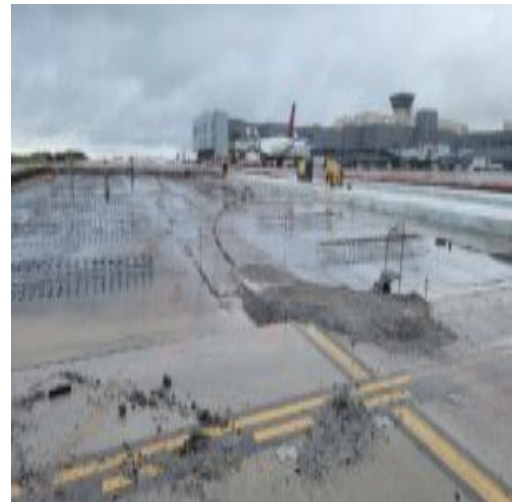


Date : 06/21/2023
Project No : 2022C106
Client Company : CWM
Arrival Time : 06/21/2023 14:00
Onsite Hours : 04:00

ASEC Report ID : 59903
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : rainy
Departure Time : 06/21/2023 18:00
ASEC Technician Name : Aminullah Azimi



At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative visited the job site to observe and monitor the contractor's work activities from a quality standpoint to assure compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:

- A pre-pour observation performed in the taxiway, phase 1A, Lane 6 and Lane 8 portions of the project this day. The contractor completed rebar and dowel basket placement for these lanes.
- The writer visually inspected the installation and setup of these lanes and advised the contractor representatives of any minor corrections that were required.
- Contractor cleaned out loose rock.
- Baskets were found to be level and straight and secured.
- Dowel bars have epoxy. Embedment depth was found to be 15" in concrete.
- Our representative along with Depto of ATLQA and the ATLNext representative Cornell did not sign the pre-pour card because in the north end, lane 8 displayed water ponding which the contractor could not remove due to inclement weather. The ATL Next rep moved the pre-pour card signature to the night shift.

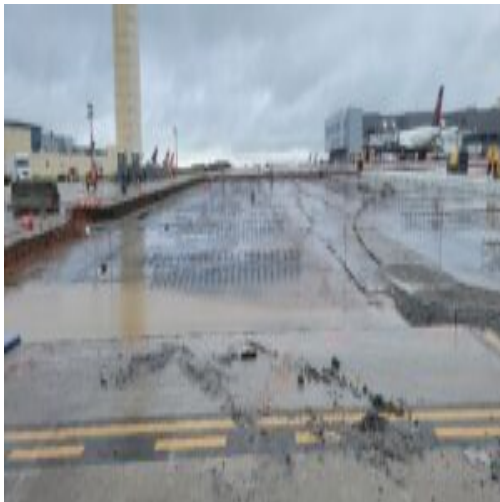

Date : 06/21/2023
Project No : 2022C106
Client Company : CWM
Arrival Time : 06/21/2023 14:00
Onsite Hours : 04:00

ASEC Report ID : 59903
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : rainy
Departure Time : 06/21/2023 18:00
ASEC Technician Name : Aminullah Azimi

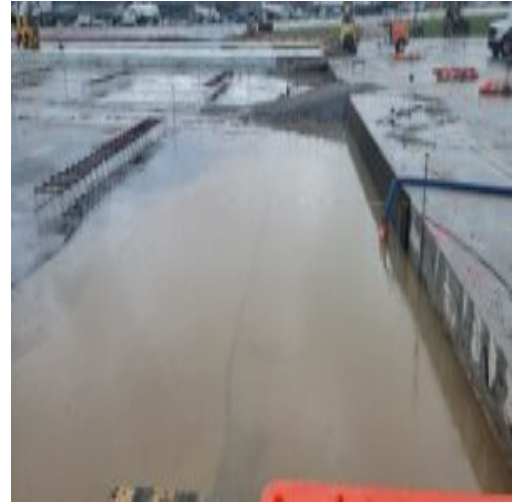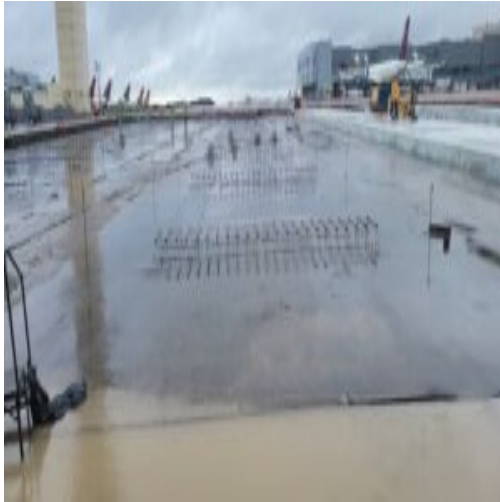

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
