

Date : 12/04/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 12/04/2025 07:30
Onsite Hours : 05:30

ASEC Report ID : 88424
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 12/04/2025 13:00
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site to observe contractor (NG Grading) for the observation/testing of the placement of fill/backfill. Upon arrival to the site, the site appeared to be frozen from low temperatures from the previous night. The contractor spent the morning stripping away any frozen ground before placing additional fill. After the sun came out, the temperatures increased and the frosted ground turned into mud. The contractor focused their efforts on Lots #8 through #13 and #52 through #60 area. After removal of frosted ground/mud, the contractor began placing lifts of approximately 6 to 8-inches in size and compacted via a sheep-foot roller. Density testing was performed, and test results were provided to the contractor.

The pipe crew began installation of pipeline in the back detention pond area. This pipeline appears to be in greenspace located along the bank and running in-between the lots. The contractor appears to be putting in a good effort to compact this area.

Contractor spent the remainder of the afternoon slicking off the site for the scheduled rain in the forecast.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



installing AA Pipeline



stripping frozen dirt

Date : 12/04/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 12/04/2025 07:30
Onsite Hours : 05:30

ASEC Report ID : 88424
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 12/04/2025 13:00
ASEC Technician Name : Sean Willett



stripping frozen ground



cut area above connexes at main entrance



compaction around AA pipeline



compaction around AA pipeline

Date : 12/04/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 12/04/2025 07:30
Onsite Hours : 05:30


ASEC Report ID : 88424
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 12/04/2025 13:00
ASEC Technician Name : Sean Willett



commercial lot area



frozen ground commercial lots

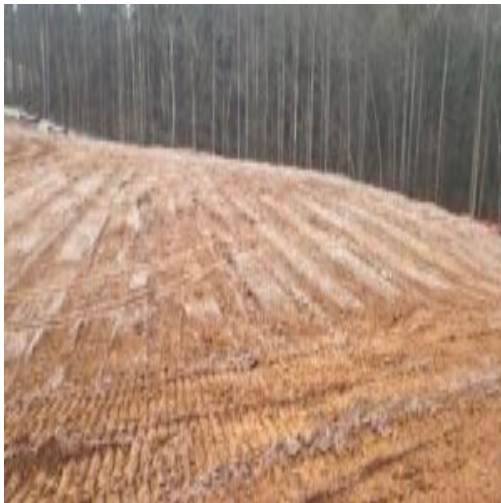

frozen ground



back detention pond area AA pipeline install

Date : 12/04/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 12/04/2025 07:30
Onsite Hours : 05:30

ASEC Report ID : 88424
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 12/04/2025 13:00
ASEC Technician Name : Sean Willett



AA pipeline back detention pond area

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
