

Date : 04/30/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 04/30/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 93864
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : sunny
Departure Time : 04/30/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.



Crew installed an 18-inch reinforced concrete pipe (RCP) between manholes B7 and B9 over a total length of 61 lineal feet. Following the pipe installation, backfill material was placed in lifts and compacted. Around the manholes, compaction was carried out using a trench compactor and a mini sheep-foot roller while a standard sheep-foot roller was used for compacting the remaining backfill along the trench. Concurrently, the crew began work at manhole B10, where excavation operations were performed, and the 24-inch RCP pipe was aligned with the existing manhole to prepare for the next phase of installation.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 04/30/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 04/30/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 93864
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : sunny
Departure Time : 04/30/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

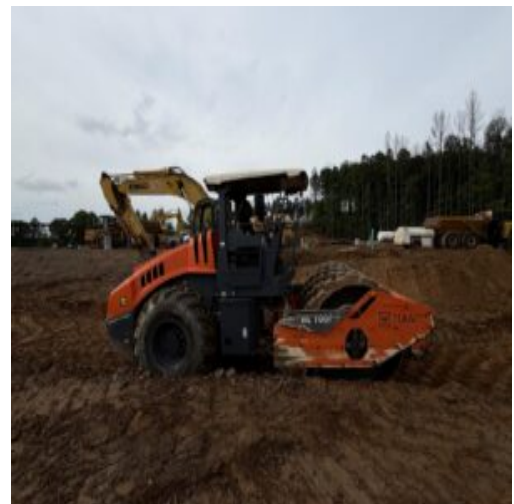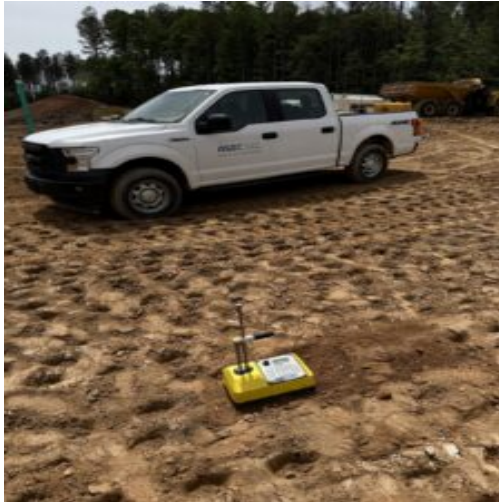

Date : 04/30/2026
Project No : 2025C260
Client Company : Artisan
Arrival Time : 04/30/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 93864
Name of the Project : NW (PHASE 2) Parkway Extension
Project Location : Dallas
Weather : sunny
Departure Time : 04/30/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
