

Date : 04/18/2023
Project No : 2023C111
Client Company : 2MATL
Arrival Time : 04/18/2023 08:00
Onsite Hours : 02:00

ASEC Report ID : 58700
Name of the Project : DOA Fiber Infrastructure Improvements
Project Location : HJAIA
Weather : Sunny
Departure Time : 04/18/2023 10:00
ASEC Technician Name : Isaac Davis

At the request of the client's representative, AS ENGINEERING AND CONSULTING, LLC (ASEC) representative, Isaac Davis visited the job site to observe and monitor the contractor's work activities from a quality standpoint to assure compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:


- The writer arrived on site to verify the subgrade for the proposed vault 2 generator pad. The generator pad is a 16' 8" X 11' 8" section and was excavated to proposed bottom of concrete elevation at this time.
- While probing the ground within the footprint, the writer noted approximately 11 feet 8 inches X 5 feet section on the north side, loose to a depth of approximately 4 to 6 inches.
- The writer recommended this area be remediated by removing the top 6-inches of this section and replacing it with structural fill or #57 stone.
- The contractor chose to replace the under-cut section with # 57 stone. The subgrade is now acceptable and ready for rebar installation.
- The form work and the bottom mat of the pad are being installed.

If you have any questions about our observations or recommendations stated in this report, we will be more than glad to discuss them with you.



Date : 04/18/2023
Project No : 2023C111
Client Company : 2MATL
Arrival Time : 04/18/2023 08:00
Onsite Hours : 02:00

ASEC Report ID : 58700
Name of the Project : DOA Fiber Infrastructure Improvements
Project Location : HJAIA
Weather : Sunny
Departure Time : 04/18/2023 10:00
ASEC Technician Name : Isaac Davis

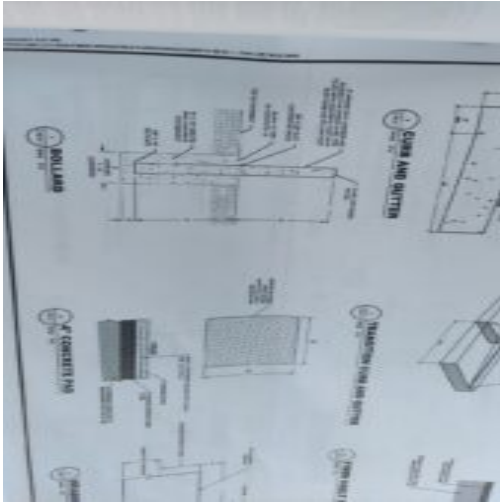

Ramchandra R. Mogulla
GA P.E. 036021
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
