

Date : 07/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/20/2026 06:30
Onsite Hours : 05:30

ASEC Report ID : 96312
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 07/20/2026 12:00
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


On the above date our representative was on site to observe and assist in and testing concrete for the pour for the bridge slab deck pour of 135 cubic yards. Assisted in molding three sets of (6) 4 x 8 cylinders. See additional report dated today by ASEC technician.

The writer reobserved placement of reinforcing steel for the bridge panels prior to concrete placement. Discrepancies observed on 7/17/26 were corrected.

The writer also observed proof-rolling of the remaining damaged subgrade soils to sanitary sewer manhole #12 using a loaded tandem dump truck loaded with 18 plus tons. The subgrade was also observed by members from NWGP who began repair measures clipping damaged subgrade soils to replace with additional base stone. The contractor clipped out a section today recommended for 4" placing six loads of base stone with contract base stone included.

Also observed the grading contractor hammering residual rock at various building lots.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

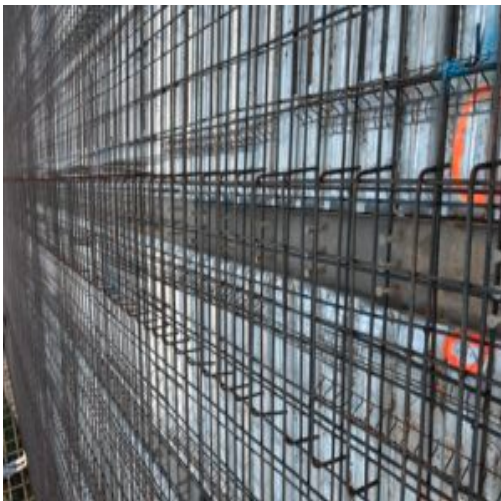

Reinforcing steel in place at panels deck



Date : 07/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/20/2026 06:30
Onsite Hours : 05:30

ASEC Report ID : 96312
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 07/20/2026 12:00
ASEC Technician Name : Clyde Smith




Resteel observations panel decks were cleaned



Sampling of placed concrete



Concrete placement at sidewalk

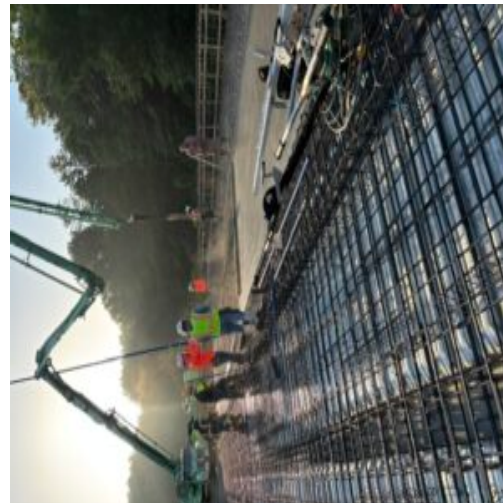

Concrete placement by pumping

Date : 07/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/20/2026 06:30
Onsite Hours : 05:30



ASEC Report ID : 96312
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 07/20/2026 12:00
ASEC Technician Name : Clyde Smith



#6 vertical bars in place at support dowel rods manhole # 12 which clipping was recommended to repair from rain events and construction traffic




Observing proof of remaining subgrade to sanitary sewer

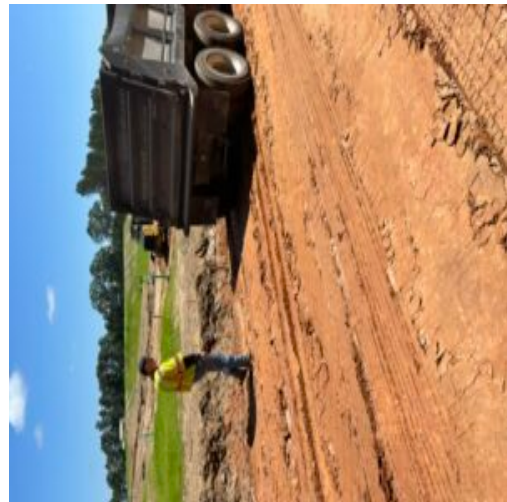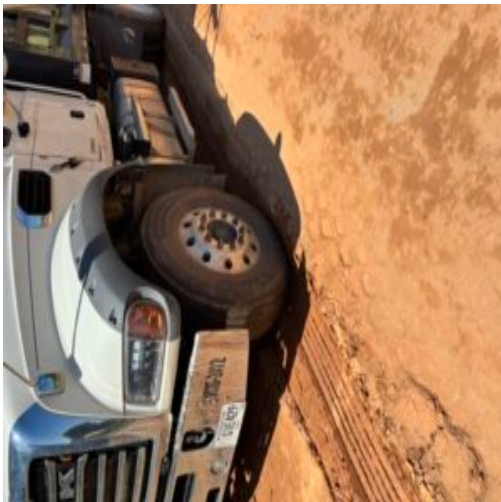

Date : 07/20/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 07/20/2026 06:30
Onsite Hours : 05:30

ASEC Report ID : 96312
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 07/20/2026 12:00
ASEC Technician Name : Clyde Smith

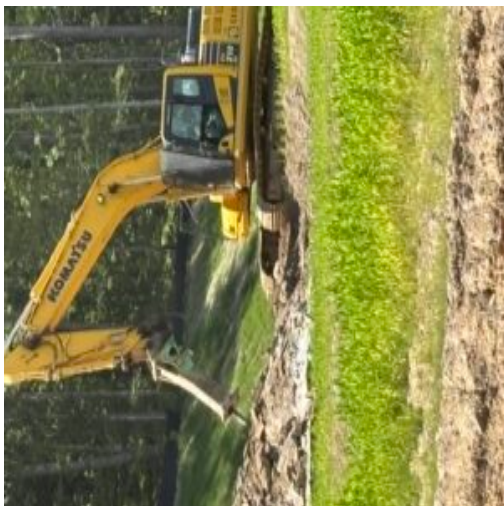

Hammering of residual rock at bldg lot

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
