

Date : 08/10/2026  
Project No : 2025C214  
Client Company : Artisan  
Arrival Time : 08/10/2026 07:30  
Onsite Hours : 11:00

ASEC Report ID : 96789  
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)  
Project Location : Dallas  
Weather : cloudy  
Departure Time : 08/10/2026 18:30  
ASEC Technician Name : Clyde Smith


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative made two trips to observe fill placement for the bridge west side abutment in the morning and performing density tests late afternoon after compacting efforts had been complete. Compaction results failed to meet project specifications and recommendations were made to use an off-road dump truck for additional compacting efforts. The contractor plans to follow recommendations and re compact tomorrow prior to re-testing. Density tests were performed at elevation -7.5 feet below the sanitary sewer installation location.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Performed density tests all areas failed

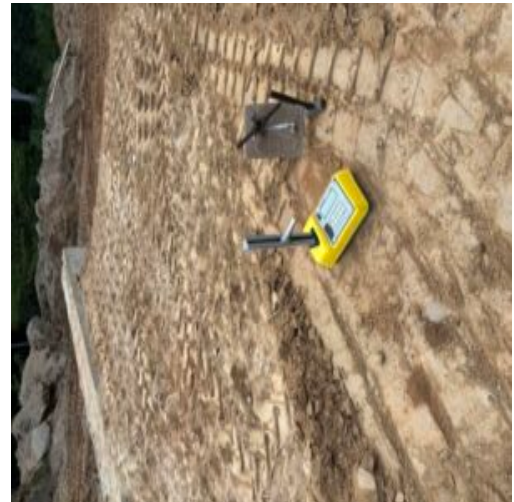

Density tests

Date : 08/10/2026  
Project No : 2025C214  
Client Company : Artisan  
Arrival Time : 08/10/2026 07:30  
Onsite Hours : 11:00

ASEC Report ID : 96789  
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)  
Project Location : Dallas  
Weather : cloudy  
Departure Time : 08/10/2026 18:30  
ASEC Technician Name : Clyde Smith





Fill and compacting efforts observed

Date : 08/10/2026  
Project No : 2025C214  
Client Company : Artisan  
Arrival Time : 08/10/2026 07:30  
Onsite Hours : 11:00

ASEC Report ID : 96789  
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)  
Project Location : Dallas  
Weather : cloudy  
Departure Time : 08/10/2026 18:30  
ASEC Technician Name : Clyde Smith



Tension rods observed at abutment wall

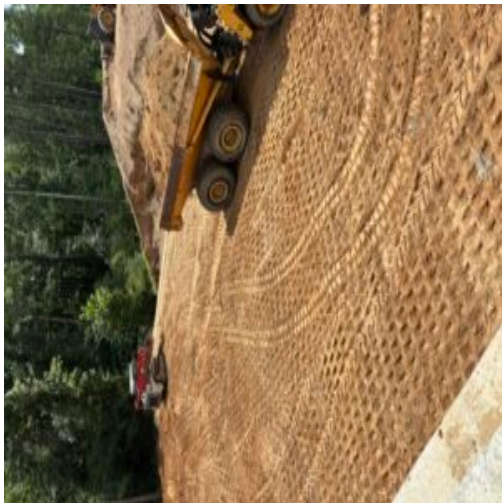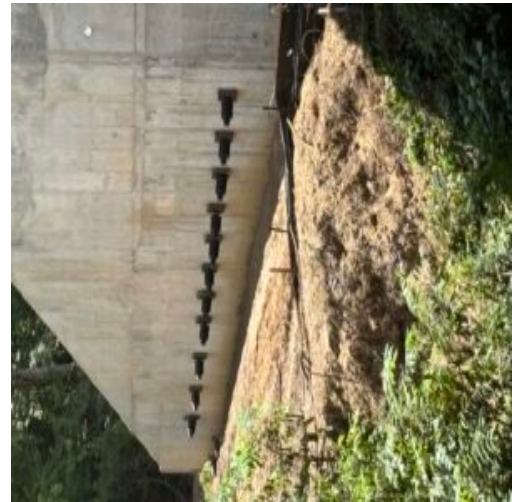

Fill placement at bridge abutment

*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
