

Date : 08/31/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 08/31/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97340
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 08/31/2026 17:30
ASEC Technician Name : Clyde Smith


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the grading contractor Thompson continue backfilling for the west side bridge abutment. The writer performed density tests using a Troxler Nuclear gauge model 3430, serial no. 91643. Compaction results were in compliance with project specifications.

The writer also observed the paving contractor NWGP continue subbase preparation at NatureWalk parkway preparing for a proof-roll on tomorrow.

The writer assisted in observing DCP tests being performed at Seven Hills Phase 13 building Lots #40 and 41. Due to a large volume of weathered rock materials used for fill it was difficult to perform the tests manually. These lots were observed and density tests performed during placement therefore, it is in the writer opinion that foundation footings are suitable for a bearing design pressure of 2000 psf.


We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

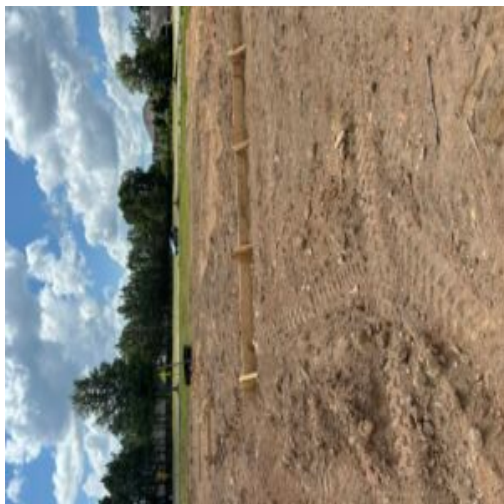

In place weathered rock materials at building lots 40 and 41. Attempted DCP tests in footings

Date : 08/31/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 08/31/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97340
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 08/31/2026 17:30
ASEC Technician Name : Clyde Smith



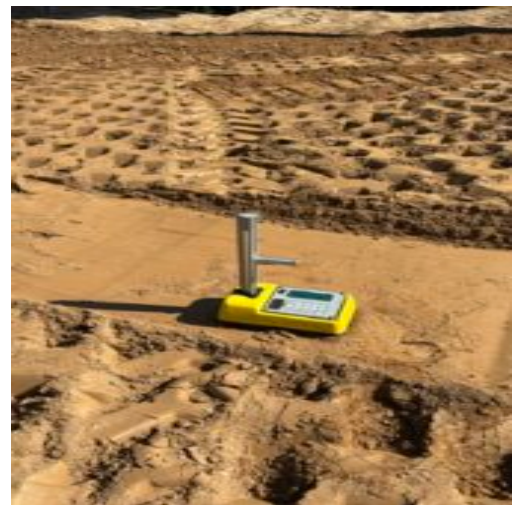


Backfill and density tests performed at west side bridge abutment



Date : 08/31/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 08/31/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97340
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 08/31/2026 17:30
ASEC Technician Name : Clyde Smith

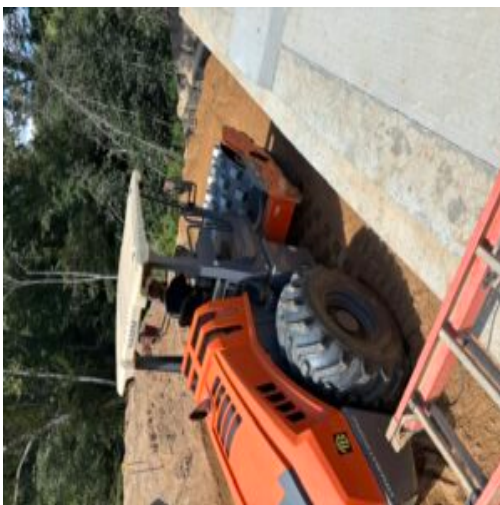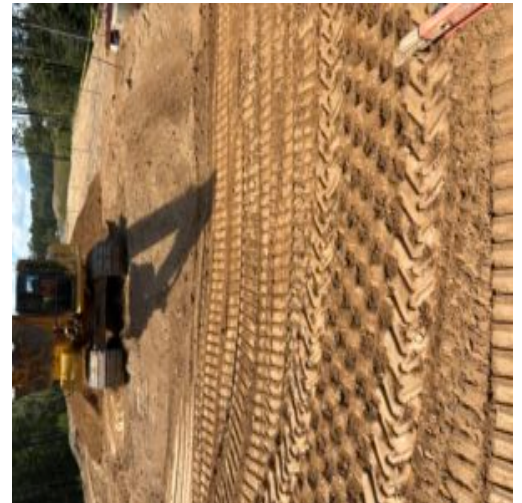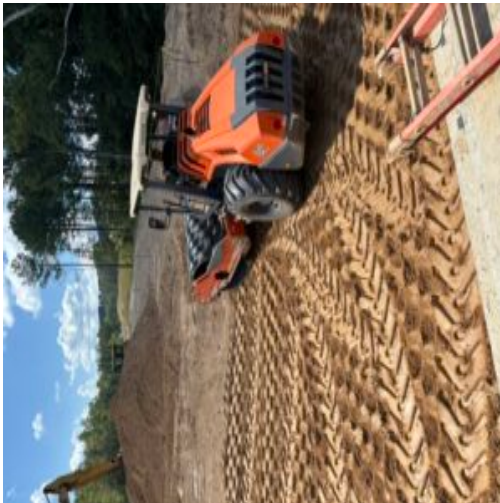



AS Engineering
and Consulting LLC

Daily Field Report

Date : 08/31/2026
Project No : 2025C214
Client Company : Artisan
Arrival Time : 08/31/2026 07:30
Onsite Hours : 10:00

ASEC Report ID : 97340
Name of the Project : NW Unit 4 BRIDGE (Materials Testing)
Project Location : Dallas
Weather : Sunny
Departure Time : 08/31/2026 17:30
ASEC Technician Name : Clyde Smith

A handwritten signature in black ink that reads 'Kenneth Mosman'.

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
