



Date : 10/03/2024
Project No : 2021C002
Client Company : CW Matthews
Arrival Time : 10/03/2024 07:00
Onsite Hours : 10:00

ASEC Report ID : 70873
Name of the Project : Runway 9L End Around Taxiway
Project Location : HJAIA
Weather : Sunny
Departure Time : 10/03/2024 17:00
ASEC Technician Name : Fawad Shagiwal

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawings/specifications, applicable codes and material submittals.

The following observations were observed on the site this day.

- Excavation of a trench for the installation and placement of a 46 foot long, 12-inch diameter water line for the fire hydrant was completed using CAT (315FL) equipment.
- The placement of No. 57 stone atop the water line for the fire hydrant was completed.
- One (1) foot lifts were placed and compacted for the trench using a trench packer (RTSC3).
- Density test results indicate that the compacted material met the project requirements of 95% the maximum dry density obtained by the (Standard Proctor ASTM 698).

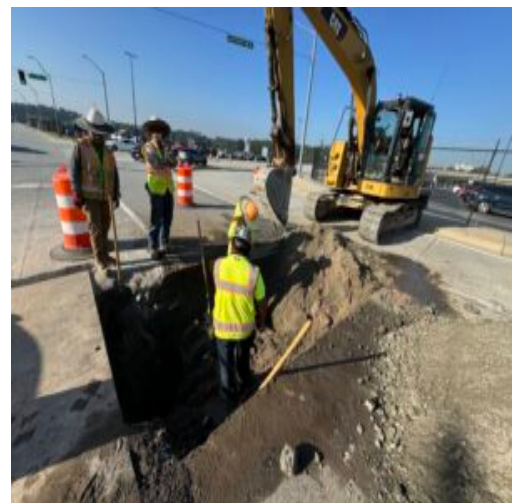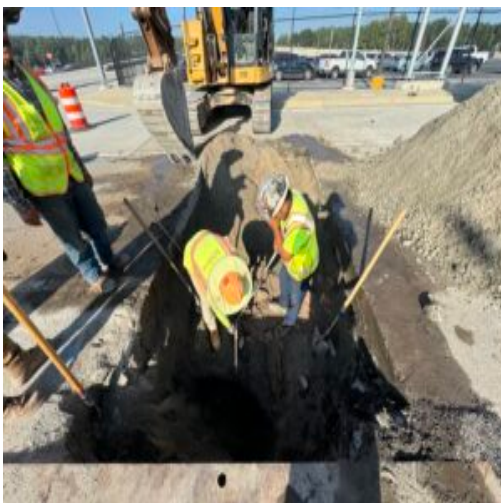

Date : 10/03/2024
Project No : 2021C002
Client Company : CW Matthews
Arrival Time : 10/03/2024 07:00
Onsite Hours : 10:00

ASEC Report ID : 70873
Name of the Project : Runway 9L End Around Taxiway
Project Location : HJAIA
Weather : Sunny
Departure Time : 10/03/2024 17:00
ASEC Technician Name : Fawad Shagiwal



Date : 10/03/2024
Project No : 2021C002
Client Company : CW Matthews
Arrival Time : 10/03/2024 07:00
Onsite Hours : 10:00

ASEC Report ID : 70873
Name of the Project : Runway 9L End Around Taxiway
Project Location : HJAIA
Weather : Sunny
Departure Time : 10/03/2024 17:00
ASEC Technician Name : Fawad Shagiwal



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
