


Date : 10/01/2024
Project No : 2021C002
Client Company : CW Matthews
Arrival Time : 10/01/2024 06:30
Onsite Hours : 11:30

ASEC Report ID : 70779
Name of the Project : Runway 9L End Around Taxiway
Project Location : HJAIA
Weather : Sunny
Departure Time : 10/01/2024 18:00
ASEC Technician Name : Fawad Shagiwal

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawings/specifications, applicable codes and material submittals.

The following observations were observed on the site this day.

- Excavation and digging of a trench (20 feet long) for the installation and placement of a 12-inch diameter water line for the fire hydrant progressed using CAT(315FL) equipment.
- The placement and installation of a 20 foot long, 12 inch in diameter water line for the fire hydrant propose progressed.
- The placement of No. 57 stone atop the water line also progressed.

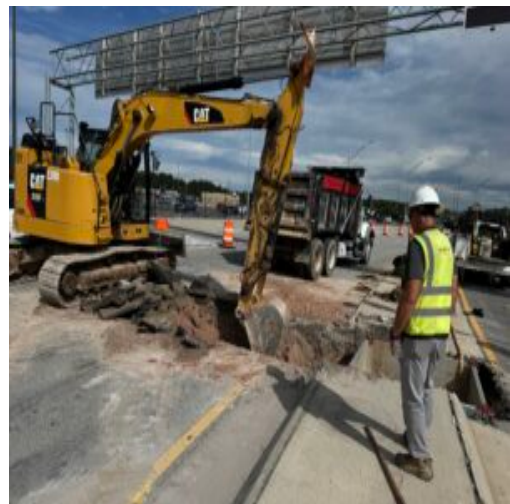

Date : 10/01/2024
Project No : 2021C002
Client Company : CW Matthews
Arrival Time : 10/01/2024 06:30
Onsite Hours : 11:30

ASEC Report ID : 70779
Name of the Project : Runway 9L End Around Taxiway
Project Location : HJAIA
Weather : Sunny
Departure Time : 10/01/2024 18:00
ASEC Technician Name : Fawad Shagiwal



Date : 10/01/2024
Project No : 2021C002
Client Company : CW Matthews
Arrival Time : 10/01/2024 06:30
Onsite Hours : 11:30

ASEC Report ID : 70779
Name of the Project : Runway 9L End Around Taxiway
Project Location : HJAIA
Weather : Sunny
Departure Time : 10/01/2024 18:00
ASEC Technician Name : Fawad Shagiwal



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
