

Date : 06/03/2023
Project No : 2022C106
Client Company : CWM
Arrival Time : 06/03/2023 19:00
Onsite Hours : 11:00

ASEC Report ID : 59697
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : rainy
Departure Time : 06/04/2023 6:00
ASEC Technician Name : Aminullah Azimi



At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative visited the job site to observe and monitor the contractor's work activities from a quality standpoint to assure compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:

- A proof-roll observation was performed in the taxiway replacement 22, phase 1B,
- A fully loaded tandem-axled dump truck was used to proof-roll the above-mentioned subgrade with multiple passes across the area.
- Severe yielding and deflection were not observed during the proof-roll at all areas mentioned above. except a small area (9×7) feet at location 70 feet south of the north end and 8 feet to east of center lane. It was recommended to undercut to the depth of 6" and replace with low slump concrete.
- Our representative along with Freed of ATLQA and the ATLNext representative Barry Miller observed the proof-roll.
- The contractor also performed the first milling.



Date : 06/03/2023
Project No : 2022C106
Client Company : CWM
Arrival Time : 06/03/2023 19:00
Onsite Hours : 11:00

ASEC Report ID : 59697
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : rainy
Departure Time : 06/04/2023 6:00
ASEC Technician Name : Aminullah Azimi

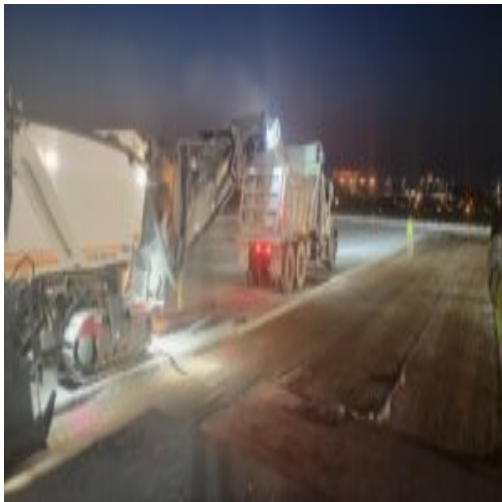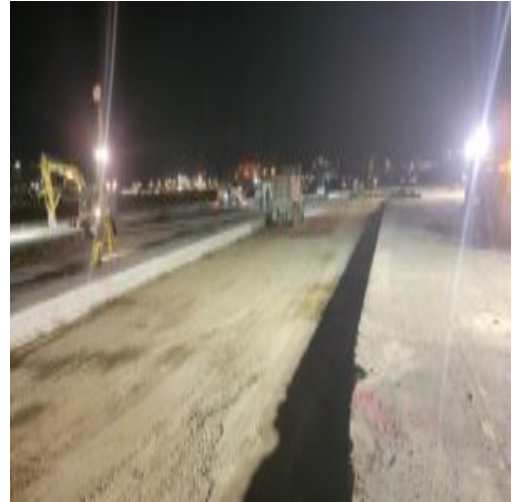

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
