


Date : 06/22/2023
Project No : 2022C106
Client Company : CWM
Arrival Time : 06/22/2023 9:00
Onsite Hours : 10:00

ASEC Report ID : 59909
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : cloudy
Departure Time : 06/22/2023 19:00
ASEC Technician Name : Aminullah Azimi

At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative visited the job site to observe the contractor's work activities from a quality standpoint to assure compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:

- A pre-pour observation was performed in the taxiway, phase 1A, Lane 1 and Lane 3 portions of the project this day. The contractor completed rebar and dowel basket placement for these lanes.
- The writer visually inspected the installation and setup of these lanes and advised the contractor representatives of any minor corrections that were required.
- Contractor cleaned loose rock and debris and puddles of water from the base.
- Baskets were found to be level and straight and secured.
- Dowel bars have epoxy. Embedment depth was found to be 15" in concrete.
- Our representative along with Jose of ATLQA and the ATLNext representative Bralin and CWM rep Brandon signed the pre-pour card.
- Placement of LS concrete will occur at locations. lane1, STA 534+00 (7'x3.5'), Lane 1, STA 533+75 (4'x4') and lane 1(STA 534+25 to STA 535+25).
- The sewer enhancement project was canceled due to the onset of inclement weather.

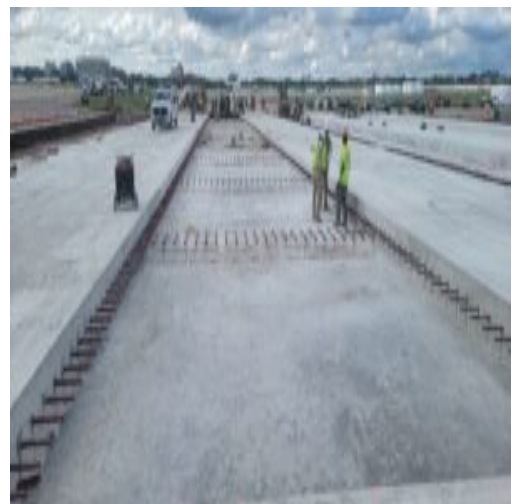

Date : 06/22/2023
Project No : 2022C106
Client Company : CWM
Arrival Time : 06/22/2023 9:00
Onsite Hours : 10:00

ASEC Report ID : 59909
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : cloudy
Departure Time : 06/22/2023 19:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
