


Date : 04/03/2024
Project No : 2022C106
Client Company : CWM
Arrival Time : 04/03/2024 8:00
Onsite Hours : 9:00

ASEC Report ID : 65853
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : sunny
Departure Time : 04/03/2024 17:00
ASEC Technician Name : Aminullah Azimi

At the request of the client's representative, AS ENGINEERING AND CONSULTING, LLC (ASEC) representative, Amin Azimi visited the job site to observe the contractor's work activities from a quality standpoint to verify compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:

- observed the subcontractor (Atlanta Paving) milling asphalt for the Taxiway phase 7.
- observed the contractor (Kelly/Cheoah) begin excavating from existing manhole Ex-1 for installation of 30" RCP running from west to east across the Taxiway; the subcontractor used a CAT 76F excavator to excavate material to haul offsite in off-road dump trucks prior to placing the trench box. The subcontractor noticed upon the demo that the existing pipe was 24" RCP instead of 30" RCP. The subcontractor had ABC contracting onsite to core the existing manhole 30"RCP. The subcontractor achieved the grade of the pipe then placed approximately 1-foot of No. 89 stone for the bedding of the pipe.
- observed the crew from Kelly/Cheoah stripping topsoil to haul offsite in off-road dump trucks from the east face of the Taxiway. After the topsoil was removed, the contractor graded the proposed taxiway on the east using a CAT bulldozer to cut the material down to subgrade and a CAT 76F excavator to place the stockpile of material cut in the area of the asphalt.

In case of any questions or concerns with regards to our observations or recommendations stated in this report we will be more than glad to discuss them with

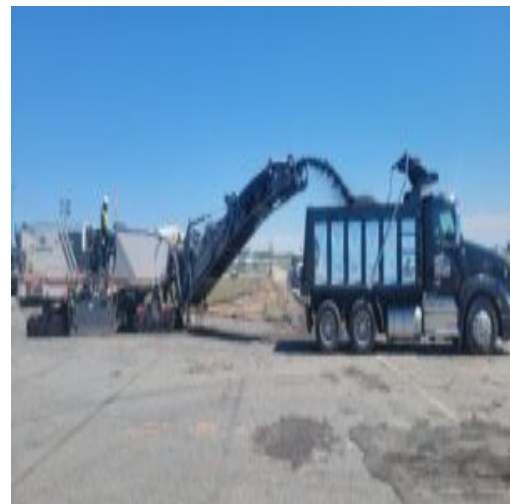

Date : 04/03/2024
Project No : 2022C106
Client Company : CWM
Arrival Time : 04/03/2024 8:00
Onsite Hours : 9:00

ASEC Report ID : 65853
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : sunny
Departure Time : 04/03/2024 17:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
