

Date : 04/08/2024
Project No : 2022C106
Client Company : CWM
Arrival Time : 04/08/2024 7:30
Onsite Hours : 10:30

ASEC Report ID : 65940
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : sunny
Departure Time : 04/08/2024 18:00
ASEC Technician Name : Aminullah Azimi

At the request of the client's representative, AS ENGINEERING AND CONSULTING, LLC (ASEC) representative, Amin Azimi visited the job site to observe the contractor's work activities from a quality standpoint to verify compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:


- A proof-roll observation was performed on the taxiway 2022 phase B.
- A fully loaded tandem-axle dump truck was used to proof-roll the above-mentioned subgrade with multiple passes across the area.
- No severe yielding and/or deflection was observed during the proof-roll at all areas mentioned above.
- Our representative along with Thomas of ATLQA and the ATLNext representative Braylyn observed the proof-roll.
- Work was being performed in the Lanes 1 and 3 portion of the project on this day. Contractor completed rebar and dowel baskets for these lanes.
- The writer verified proper installation and setup of this lanes 1 and 3, advised the contractor representatives of any minor corrections that may be needed.
- BBH installed and poured concrete for duct bank between MH A-1 and MH A-2.
- CWM was pouring flow fill for the existing manhole.
- ATL Paving was placing GAB for CTB use.
- In addition to this, the writer assisted and observed straight edge testing of phase A on CT.

In case of any questions or concerns with regards to our observations or recommendations stated in this report we will be more than glad to discuss them with you.



Date : 04/08/2024
Project No : 2022C106
Client Company : CWM
Arrival Time : 04/08/2024 7:30
Onsite Hours : 10:30

ASEC Report ID : 65940
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : sunny
Departure Time : 04/08/2024 18:00
ASEC Technician Name : Aminullah Azimi

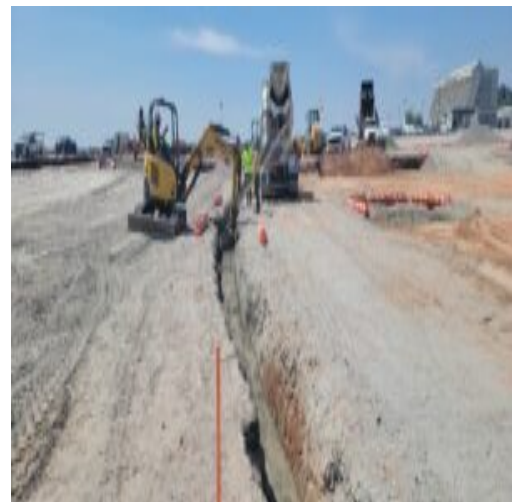

Date : 04/08/2024
Project No : 2022C106
Client Company : CWM
Arrival Time : 04/08/2024 7:30
Onsite Hours : 10:30

ASEC Report ID : 65940
Name of the Project : Taxiway 2022 Pavement Replacement
Project Location : HJAIA
Weather : sunny
Departure Time : 04/08/2024 18:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
