


Date : 03/04/2024
Project No : 2022C165
Client Company : Toll Bros. Inc.
Arrival Time : 03/04/2024 13:00
Onsite Hours : 03:00

ASEC Report ID : 64617
Name of the Project : Northfield @ Polo Fields - Phase2
Project Location : Pittman Road, Cumming, GA
Weather : cloudy
Departure Time : 03/04/2024 16:00
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

- The placement and compaction of backfill soils for the sewer pipe trench between MH A3 to MH A4, continued this day.
- At the time of arrival, our representative observed that work was in progress with 1-foot lifts being placed and compacted using trench and sheep-foot (CP56B) compaction equipment. General probing using a 3/8" diameter probe rod was also performed.
- Density test results indicate that the compacted materials met the project requirement of 90% of the maximum dry density obtained by the (Standard Proctor ASTM 698),

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

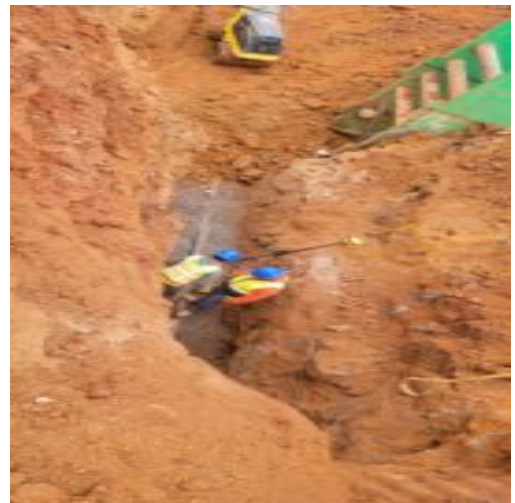

Date : 03/04/2024
Project No : 2022C165
Client Company : Toll Bros. Inc.
Arrival Time : 03/04/2024 13:00
Onsite Hours : 03:00

ASEC Report ID : 64617
Name of the Project : Northfield @ Polo Fields - Phase2
Project Location : Pittman Road, Cumming, GA
Weather : cloudy
Departure Time : 03/04/2024 16:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
