

Date : 04/16/2023
Project No : 2022C178
Client Company : CW Matthews
Arrival Time : 04/16/2023 12:00
Onsite Hours : 07:00

ASEC Report ID : 58620
Name of the Project : Ramp 2 Pavement Replacement
Project Location : HJAIA
Weather : cloudy
Departure Time : 04/16/2023 19:00
ASEC Technician Name : Aminullah Azimi

At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative, Amin Azimi visited the job site to observe and monitor the contractor's work activities from a quality standpoint to assure compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:


- Pre-pour observation performed in the Lane 1 and lane 3 portions of the project on this day. Contractor completed rebar and dowel basket placement for these lanes.
- The writer visually inspected the installation and setup of these lanes and advised the contractor representatives of any minor corrections that were needed.
- The contractor cleaned loose rock and debris and standing water from the base.
- Baskets were found to be level, straight and secured.
- Dowel bars were found to have epoxy. Embedment length was found to be 15 inches into concrete.
- The writer along with Saketh of ATLQA and ATLNext representative Craig Garland and CWM rep Brandon signed the pre-pour card.

In case of any questions or concerns with regards to our observations or recommendations stated in this report we will be more than glad to discuss them with you.



Date : 04/16/2023
Project No : 2022C178
Client Company : CW Matthews
Arrival Time : 04/16/2023 12:00
Onsite Hours : 07:00

ASEC Report ID : 58620
Name of the Project : Ramp 2 Pavement Replacement
Project Location : HJAIA
Weather : cloudy
Departure Time : 04/16/2023 19:00
ASEC Technician Name : Aminullah Azimi

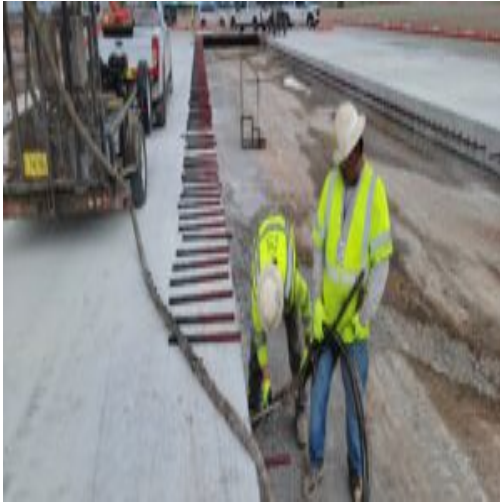

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
