


Date : 08/14/2023
Project No : 2022C218
Client Company : CW Matthews
Arrival Time : 08/14/2023 9:00
Onsite Hours : 08:00

ASEC Report ID : 60869
Name of the Project : Ramp 20 Pavement Replacement -
IFB-1230102
Project Location : HJAIA
Weather : sunny
Departure Time : 08/14/2023 17:00
ASEC Technician Name : Aminullah Azimi

At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative visited the job site to observe the contractor's work activities from a quality standpoint to verify compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:

- A pre-pour observation was performed in the Ramp 20, phase 3, Lane 1 and Lane 10, portions of the project this day. The contractor completed rebar and dowel basket placement for these lanes.
- The writer visually inspected the installation and setup of these lanes and advised the contractor representatives of any minor corrections that were required.
- Contractor cleaned loose rock and debris and puddles of water from the base.
- Baskets were found to be level and straight and secured as per job specifications.
- Dowel bars have epoxy. Embedment depth into the concrete was found to be 15 inches.
- Our representative along with Ashud of ATLQA and the ATLNext representative Cornel and CWM rep Brandon signed the pre-pour card.

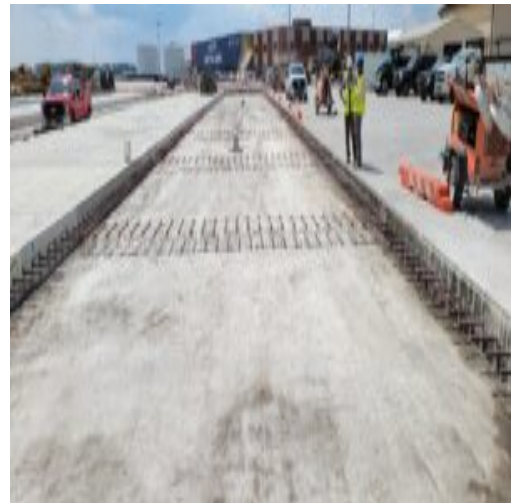

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
