


Date : 11/07/2023
Project No : 2022C218
Client Company : CW Matthews
Arrival Time : 11/07/2023 8:00
Onsite Hours : 9:00

ASEC Report ID : 62949
Name of the Project : Ramp 20 Pavement Replacement -
IFB-1230102
Project Location : HJAIA
Weather : sunny
Departure Time : 11/07/2023 17:00
ASEC Technician Name : Aminullah Azimi



At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative, Amin Azimi visited the job site to observe the contractor's work activities from a quality standpoint to verify compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made on site this shift:

- A pre-pour observation performed in the Ramp 20, phase 4, Lane 15 and utility panel at line 15 on this day. The contractor completed rebar and dowel basket placement for this lane.
- The writer visually inspected the installation and setup of these lanes and advised the contractor representatives of any minor corrections that were required.
- Contractor cleaned loose rock and debris and puddles of water from the base.
- Baskets were found to be level and straight and secured.
- Dowel bars have epoxy. Embedment depth was found to be 15" into concrete.
- The reinforcing steel was checked for correct size, number of bars, location of bars, spacing, cleanliness, support against displacement, splicing, clearance and steel grade. Based on visual observations and field measurements, appeared to be acceptable for size, spacing and quantity.
- Our representative along with Ashud of QA and Hazim the ATLNext representative and CWM rep Brandon signed the pre-pour card.
- Observed the placement of backfill soils for end around between STA 7021+75 to STA 7022+50. Density testing was performed using a Troxler nuclear gauge (#3430, serial #85759). Test results indicated that the compacted material met project requirement of 90% of the maximum dry density.

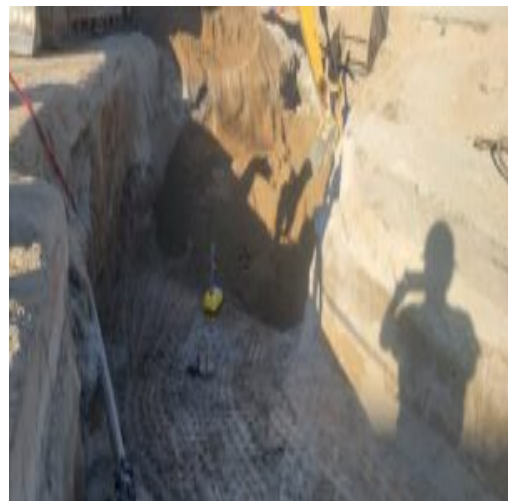

Date : 11/07/2023
Project No : 2022C218
Client Company : CW Matthews
Arrival Time : 11/07/2023 8:00
Onsite Hours : 9:00

ASEC Report ID : 62949
Name of the Project : Ramp 20 Pavement Replacement -
IFB-1230102
Project Location : HJAIA
Weather : sunny
Departure Time : 11/07/2023 17:00
ASEC Technician Name : Aminullah Azimi

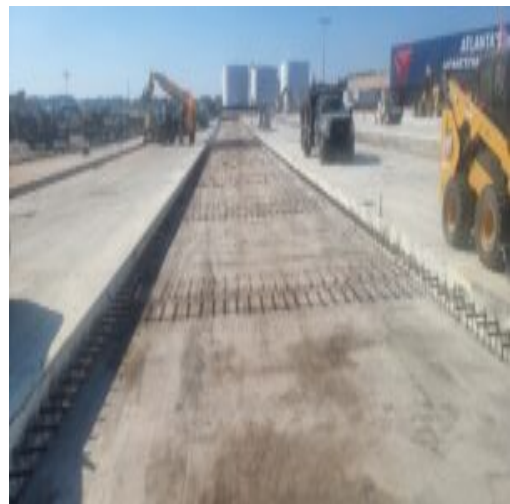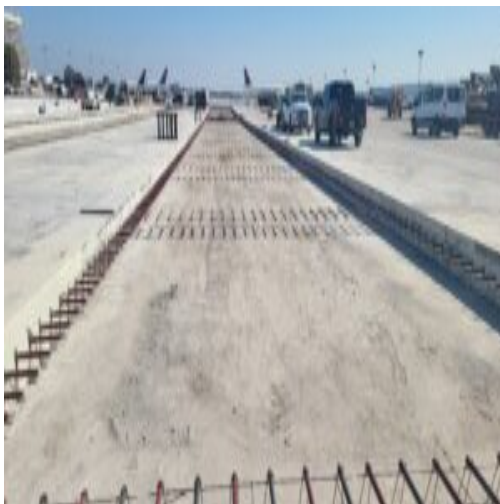

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
