

Date : 02/16/2023
Project No : 2022C227
Client Company : Artisan
Arrival Time : 02/16/2023 9:00
Onsite Hours : 05:00

ASEC Report ID : 57189
Name of the Project : Riverwalk Manor (CMT) Unit 2, PH 4E
and 4F
Project Location : Dallas
Weather : cloudy
Departure Time : 02/16/2023 14:00
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by the AS Engineering and Consulting (ASEC) representative noted above, for the purpose of providing quality control inspection and testing services, visual observation techniques were employed to assure compliance with project drawing/specifications, applicable codes, and materials submittals. the following observations were observed on site this day.

Contractor continued backfill and compaction for Lot 425 and road, upon arrival work was already in progress contractor was performing lifts, each lift being 8 inches. The soils observed on this date appear to be placed in accordance with project drawings and specifications.

The Soil was brought in using 2 dump trucks; spread was done by Komatsu 51 pxi and at depth about 14 feet below finish grade were compacted using a caterpillar 815 F.


Density testing was performed using a Troxler nuclear gauge (#3430, serial #85759). tests result indicated that the compacted material met project requirement of 90% of the maximum dry density obtained by the (Standard Proctor ASTM 698).

Density testing result:

P-01 proctor- 100.4@18.6%


T1-elevation at finish grade@ lot 425, Yd 97.8 M%15.7, Compaction:97.4%

T2-elevation at finish grade@ road, Yd 99.8 M%15.7, Compaction: 99.4%

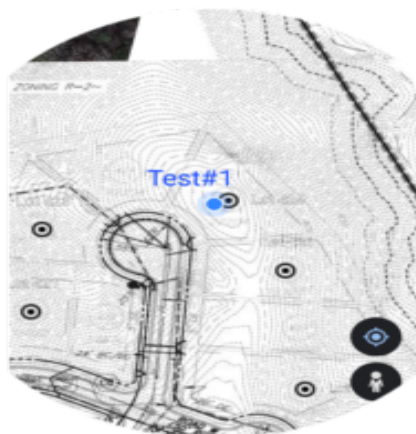

Date : 02/16/2023
Project No : 2022C227
Client Company : Artisan
Arrival Time : 02/16/2023 9:00
Onsite Hours : 05:00


ASEC Report ID : 57189
Name of the Project : Riverwalk Manor (CMT) Unit 2, PH 4E
and 4F
Project Location : Dallas
Weather : cloudy
Departure Time : 02/16/2023 14:00
ASEC Technician Name : Aminullah Azimi

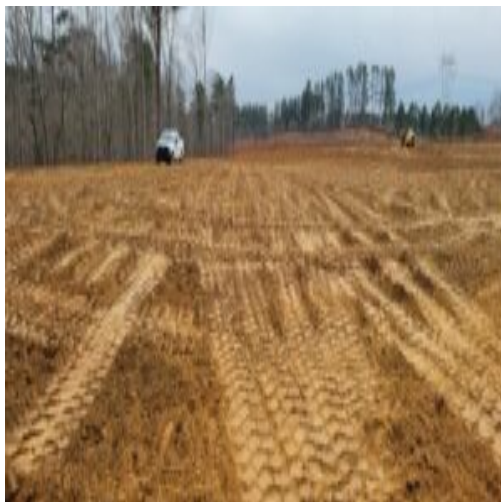

Daily Field Report

Date : 02/16/2023
Project No : 2022C227
Client Company : Artisan
Arrival Time : 02/16/2023 9:00
Onsite Hours : 05:00

ASEC Report ID : 57189
Name of the Project : Riverwalk Manor (CMT) Unit 2, PH 4E
and 4F
Project Location : Dallas
Weather : cloudy
Departure Time : 02/16/2023 14:00
ASEC Technician Name : Aminullah Azimi

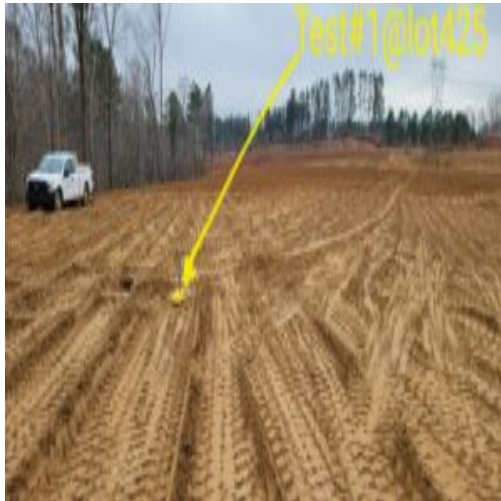

Ramchandra R. Mogulla
GA P.E. 036021
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
