

Date : 03/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/20/2023 06:00
Onsite Hours : 10:00


ASEC Report ID : 57951
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 03/20/2023 16:00
ASEC Technician Name : Vidal Dias

Our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Vidal Dias visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to observe, verify and document the ongoing project activities. (Reference drawing E720661 S1 - R5 & E720659 S1-R5.)


During the visit, the following observations were made:

1. One thousand five hundred (1500) square feet of fabric was placed along the top of the eastern retaining wall in sections H6 & G6 (drawing E720659 S1-R5) and section A6 (drawing E720661 S1 - R5).
2. Six (6) concrete blocks were placed approximately six (6) feet from the edge of the retaining wall in section H6 (drawing E720659 S1-R5.), The blocks are highlighted as yellow rectangles on the drawing.
3. Rip-Rap was placed atop the fabric in accordance with ITP-003. The area is highlighted in red on the drawing. Stones that toppled over the wall during placement were recovered after completion.
4. One hundred sixty-two (162) cubic yards of fill material (9 loads) were placed along the east boundary of section F6 to construct the slope. The slope extends approximately ten (10) feet into section F5. The area is highlighted in purple on the drawing.
5. Three hundred forty-two (342) cubic yards of fill material were placed in the basement, according to ITP-001.

Photo documentation is included below:

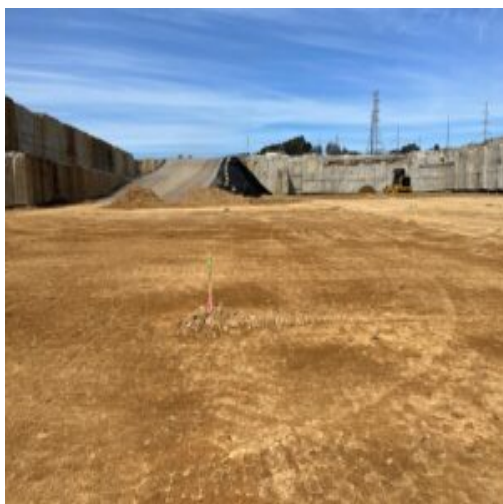

The lower half of the basement is being rolled.

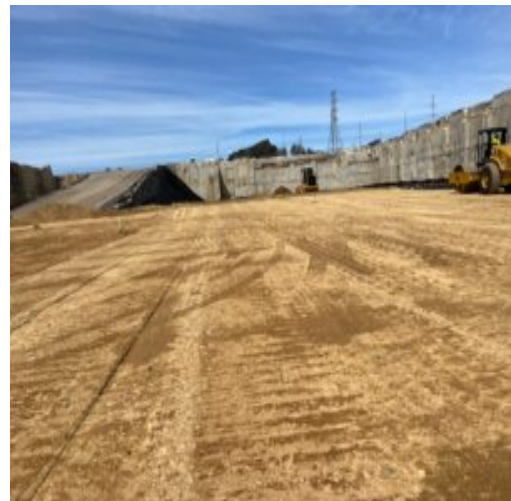

Fill being placed in upper half of basement near admin wall and compacted.

Date : 03/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/20/2023 06:00
Onsite Hours : 10:00

ASEC Report ID : 57951
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 03/20/2023 16:00
ASEC Technician Name : Vidal Dias



Riprap placed in section H6



Fabric placed in section H6



Concrete blocks placed in H6




The slope being constructed in section F6

Date : 03/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/20/2023 06:00
Onsite Hours : 10:00

ASEC Report ID : 57951
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 03/20/2023 16:00
ASEC Technician Name : Vidal Dias



Fill is being placed in the basement as seen from the top of the east wall.

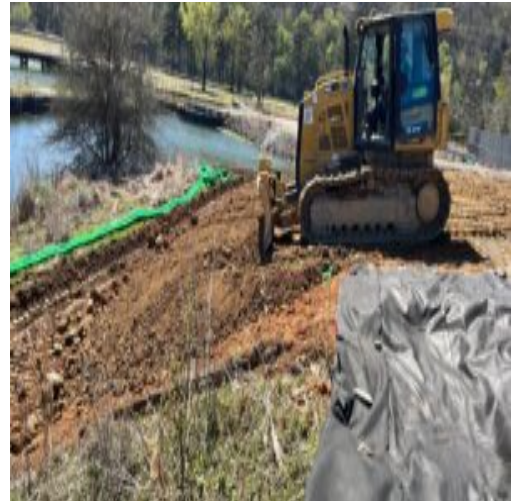

Slope construction in F6 during at 1000hrs.




Slope construction at 1400 hrs




Slope construction at 1410hrs

Date : 03/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/20/2023 06:00
Onsite Hours : 10:00

ASEC Report ID : 57951
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 03/20/2023 16:00
ASEC Technician Name : Vidal Dias

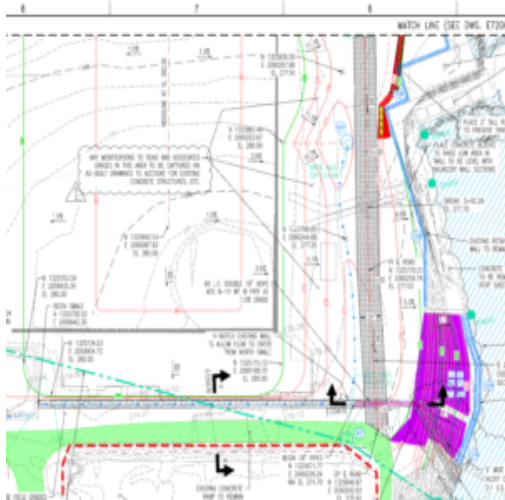

Riprap: Red Blocks: Yellow Fill: Purple

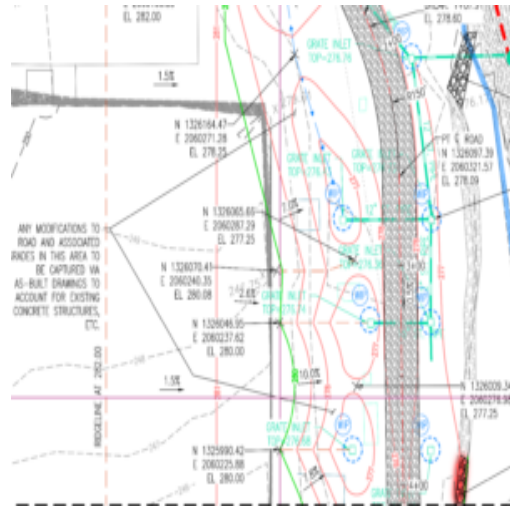

Riprap: Red

Vidal Dias

Vidal Dias
070321636
Project Geologist



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
