

Date : 03/16/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/16/2023 06:00
Onsite Hours : 10:30


ASEC Report ID : 57855
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather :
Departure Time : 03/16/2023 16:30
ASEC Technician Name : Vidal Dias

Our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Vidal Dias visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to observe, verify and document the ongoing project activities.

During the visit, the following observations were made:

1. 774 Yards (43 loads) of clay material were received and placed in the basement at sections H7 and H8.
2. The fill material was placed and compacted in the basement in accordance with ITP-001.
3. 825B and crushed concrete were placed in sections H6, G6, and F6, compacted using CAT CS54B, and proof-rolled using a tandem axle water truck. The proof-rolled area is highlighted in purple on the attached drawing.
4. During the proof roll, no significant rutting or deflection was revealed except in an area approximately 20-30 feet near the embankment adjacent to the intake canal in Baker's Creek. The area is highlighted in red on the attached drawing; these areas were marked on-site with white paint. This area is not acceptable for the placement of planned pavement.

Photo documentation is included below:

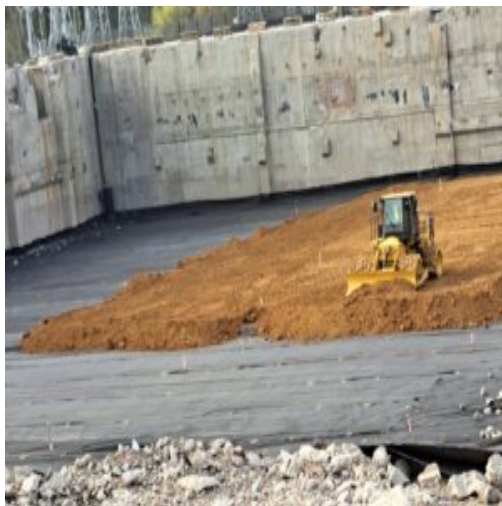

Fill material being compacted in basement



Area H6 being compacted

Date : 03/16/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/16/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 57855
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather :
Departure Time : 03/16/2023 16:30
ASEC Technician Name : Vidal Dias




Crushed concrete being placed near the inlet in H6



Crushed concrete being placed



Water truck conducting proof roll in area H6

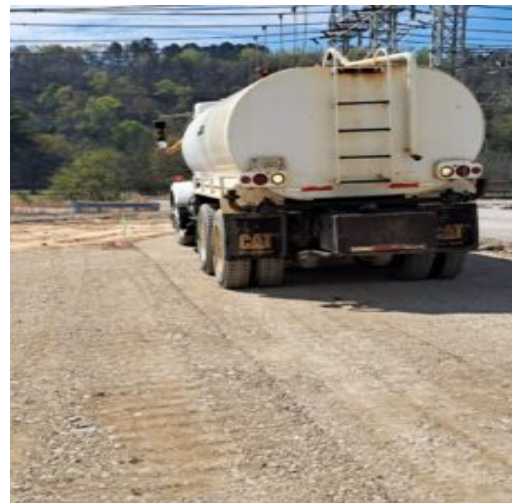

Water truck conducting proof roll in area G6

Date : 03/16/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/16/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 57855
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather :
Departure Time : 03/16/2023 16:30
ASEC Technician Name : Vidal Dias



Rutting in area F6.



Date : 03/16/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/16/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 57855
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather :
Departure Time : 03/16/2023 16:30
ASEC Technician Name : Vidal Dias



Vidal Dias
070321636
Project Geologist



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
