

Date : 03/27/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 03/27/2023 06:00
Onsite Hours : 10:00



ASEC Report ID : 58094
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 03/27/2023 16:00
ASEC Technician Name : Vidal Dias

Our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Vidal Dias visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to observe, verify and document the ongoing project activities. (Reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. Due to inclement weather and saturated subgrades, no fill materials were placed in the basement.
2. The contractor placed two hundred (200) tons of 825B in section F6 on the gravel road in accordance with ITP-003

Photo documentation and test locations are attached:

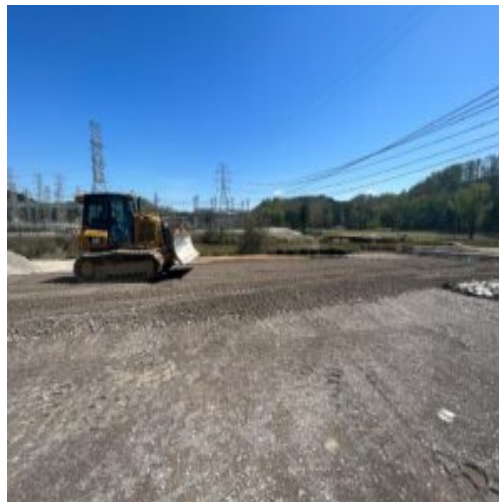

Vidal Dias
070321636
Project Geologist



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
