

Date : 04/24/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 04/24/2023 05:30
Onsite Hours : 10:30


ASEC Report ID : 58866
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 04/24/2023 16:00
ASEC Technician Name : Vidal Dias

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Vidal Dias visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. One thousand eight hundred and ninety (1890) cubic yards of fill materials were received and placed for lift five (5) in section 2 area G7 (drawing E720659) of the basement, and lift eight (8) section one (1) area B7 (drawing E720661). The materials were placed in accordance with ITP-001, and the fill area is highlighted in blue on the attached drawing.
2. Three moisture density tests were performed in section 1, area B7 (E720661 S1 - R5); the testing locations are marked on the attached drawing.
3. All three tests passed compaction and tests two and three were within optimum moisture. Test one was 1% below moisture; water was applied to the area. The section was retested, and moisture increased to 15%, which meets the specifications.

Test results are shown below:

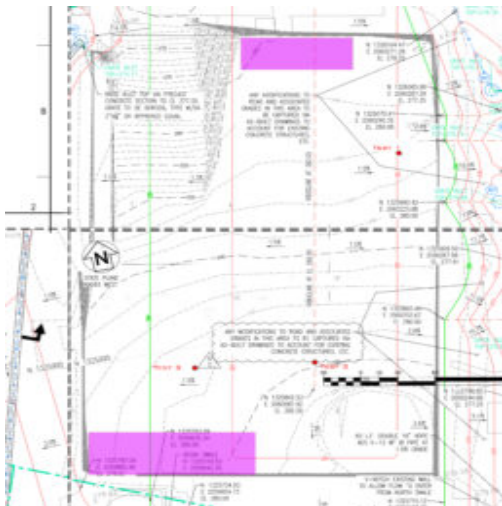

Date : 04/24/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 04/24/2023 05:30
Onsite Hours : 10:30

ASEC Report ID : 58866
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 04/24/2023 16:00
ASEC Technician Name : Vidal Dias



Vidal Dias
070321636
Project Geologist



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
