

Date : 04/29/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 04/29/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 58972
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 04/29/2023 16:30
ASEC Technician Name : Avinash Bandham


AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. Two thousand (2394) cubic yards of fill materials were received and placed for lift (7) in section 2 basement area G7 (drawing E720661) of the basement. The materials were placed and compacted in compliance with ITP-001.



2394 cub. Yds of fill material were placed

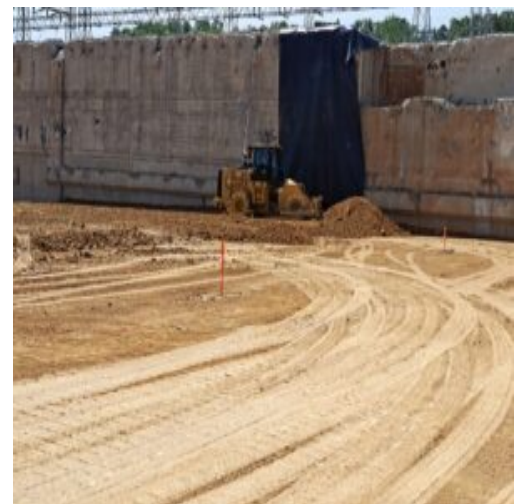

Date : 04/29/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 04/29/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 58972
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 04/29/2023 16:30
ASEC Technician Name : Avinash Bandham



compacting the section-2 basement area G7 using the roller and dozer.



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
