


Date : 05/10/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 05/10/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59201
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 05/10/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (Reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. One thousand one hundred and fifty-two (1152) cubic yards of fill materials were placed for lift (11) in section 1 area B7 (drawing E720661) of the basement. The materials were placed in accordance with ITP-001, and the fill area is highlighted in blue on the attached drawing.
2. The left-over placement of fill materials for the section 2 basement area was finished this morning.
3. The area was probed, and three density tests were performed in section 1 and 2 area G7 (E720659 S1 - R5).
4. Soil sample for a Proctor check was collected from the vicinity of test location 3.
5. Test results are listed within the Density test report of this day.

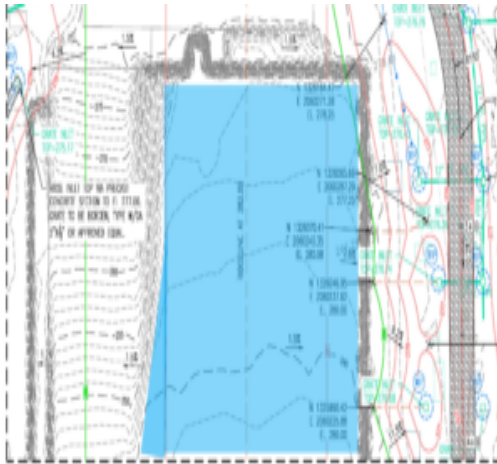

Date : 05/10/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 05/10/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59201
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 05/10/2023 16:30
ASEC Technician Name : Avinash Bandham



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
