



Date : 06/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/20/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59847
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : PARTLY CLOUDY
Departure Time : 06/20/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandham visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R8, E720659 S1-R8.)

During the visit, the following observations were made:

1. One thousand five hundred and forty-eight (1548) cubic yards of fill materials were placed for lift (14) in section 2 part 2 area G7 (E720659 S1-R8) of the basement and completed the lift and the new lift in the Section 1 basement area G7 (E720661 S1 - R8). The materials were placed and compacted in accordance with ITP-001, and the fill area is highlighted in brown as depicted in the attached drawing.
2. The area was probed with a hand probe and three moisture density nuclear gauge tests were performed in the basement, section 1 and section 2 and verified the results by running a check-plug. The test locations are depicted in the enclosed drawing.

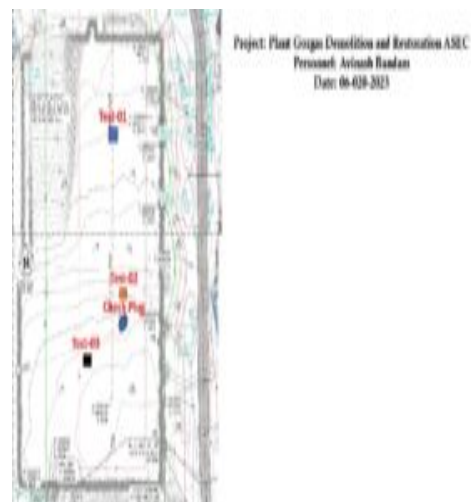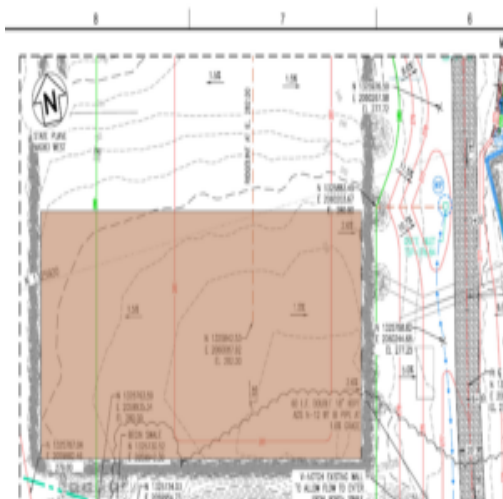

Date : 06/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/20/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59847
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : PARTLY CLOUDY
Departure Time : 06/20/2023 16:30
ASEC Technician Name : Avinash Bandham



Date : 06/20/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/20/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59847
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : PARTLY CLOUDY
Departure Time : 06/20/2023 16:30
ASEC Technician Name : Avinash Bandham



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
