

Date : 06/22/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/22/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59885
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : PARTLY CLOUDY
Departure Time : 06/22/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R8, E720659 S1-R8.)

During the visit, the following observations were made:

1. One thousand and six (1206) cubic yards of fill materials were placed for lift (16) in section 1 area B7 (E720661 S1-R8) and started and continued to the section 2 part 1 of the basement. The materials were placed and compacted in accordance with ITP-001, and the fill area is highlighted in brown as depicted in the attached drawing.
2. No testing was performed on this day. Testing of section 1 and section 2 is planned to be performed the next day or at the completion of the entire lift. Therefore, no density reports were generated on this day.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.





Date : 06/22/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/22/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59885
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : PARTLY CLOUDY
Departure Time : 06/22/2023 16:30
ASEC Technician Name : Avinash Bandham



Date : 06/22/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/22/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 59885
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : PARTLY CLOUDY
Departure Time : 06/22/2023 16:30
ASEC Technician Name : Avinash Bandham

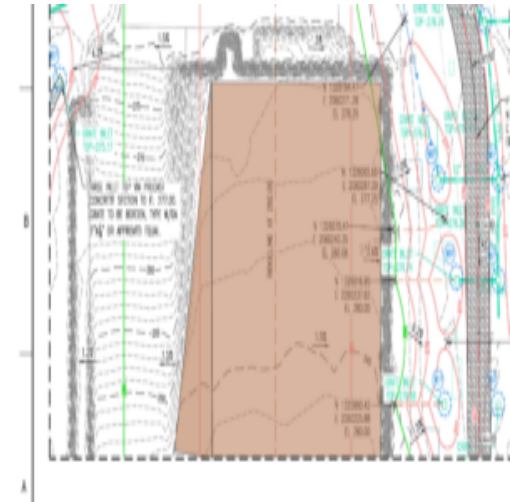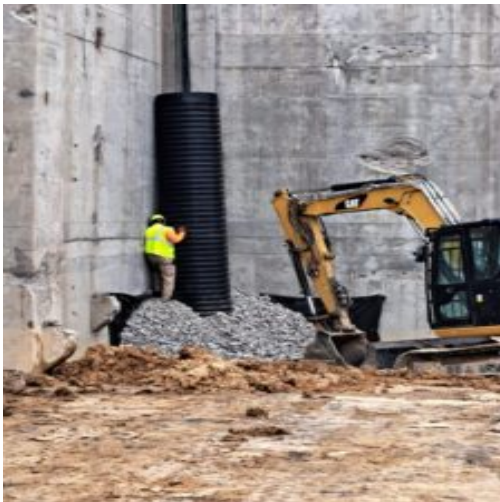

Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
