


Date : 06/21/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/21/2023 06:00
Onsite Hours : 05:00

ASEC Report ID : 59871
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : RAINY
Departure Time : 06/21/2023 11:00
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R8, E720659 S1-R8.)

During the visit, the following observations were made:

1. Six hundred and thirty (630) cubic yards of fill materials were placed for lift (16) in section 1 area B7 (E720661 S1-R8) of the basement. Fill was placed and compacted in accordance with ITP-001, and the fill area is highlighted in brown in the attached drawing.
2. The work in the basement and the hauling has been suspended on account of rainfall.

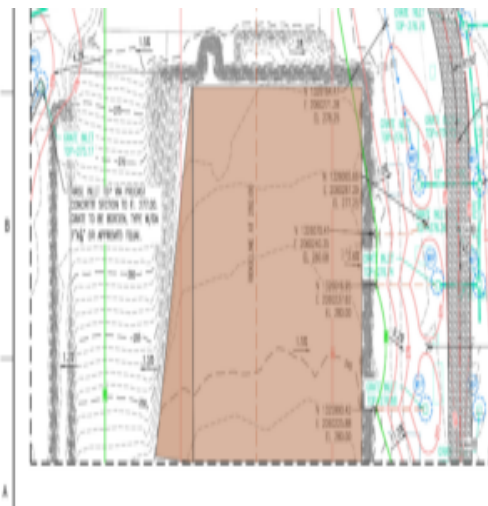

Date : 06/21/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 06/21/2023 06:00
Onsite Hours : 05:00

ASEC Report ID : 59871
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : RAINY
Departure Time : 06/21/2023 11:00
ASEC Technician Name : Avinash Bandham



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
