

Date : 09/07/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/07/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61437
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/07/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (Reference drawing E720661 S1 - R8, E720659 S1-R8.)


During the visit, the following observations were made:

1. Two thousand five hundred and ninety-two (2592) cubic yards of structural-fill materials were placed for lift (4) in section 1 basement area B7 (E720661 S1-R8) and for lift (4) in section 2 basement are G7(E720659 S1-R8). The materials were placed and compacted in accordance with ITP-001, and the fill area is highlighted in brown as depicted in the attached drawing.
2. The basement area was probed using the hand probe and three moisture density tests were performed in the basement followed with a check-plug to verify Proctor curve application. The test locations were marked on the enclosed drawing.
3. Placement of Geo-fabric and perforated pipe for the Trench drain.
4. The aggregate and pipe was into a burrito with the Geo-fabric which was initially placed in the trench.
5. Finally, a course of 57-Stone was placed on top of the covered fabric.

We appreciate the opportunity to provide our services on this project. Should you have any inquiries or require further discussion about this report, please feel free to contact us. We remain available to address any questions or concerns you may have.



Placement of Structural fill materials in section 2

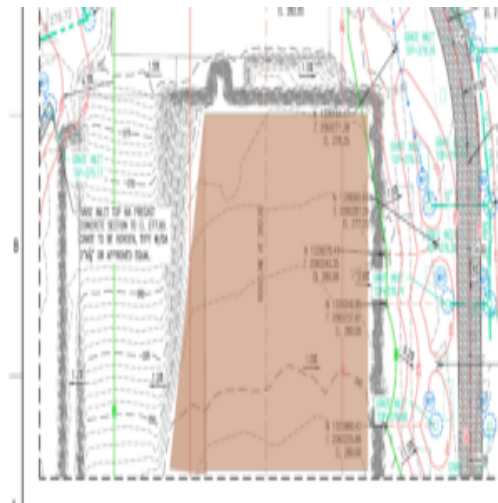

Placement of Structural fill materials in section 1

Date : 09/07/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/07/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61437
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/07/2023 16:30
ASEC Technician Name : Avinash Bandham



Placed 57-Stone along the trench drain water treatment area



Placed 57-Stone at trench drain water treatment area

Date : 09/07/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/07/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61437
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/07/2023 16:30
ASEC Technician Name : Avinash Bandham



Placed aggregate in the trench after the placement of HDPE pipe was placed in the trench after the Geo-fabric placement.



HDPE pipe was placed in the trench after the Geo-fabric placement.



Perforated pipe was placed in the trench after the Geo-fabric placement.



HDPE pipe was placed in the trench after the Geo-fabric placement.

Date : 09/07/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/07/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61437
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/07/2023 16:30
ASEC Technician Name : Avinash Bandham



placement of structural fill materials in section near
the ramp



placement of structural fill materials in section
near the ramp



Placed aggregate in the trench after the placement of
perforated pipe



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
