

Date : 09/06/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/06/2023 6:00
Onsite Hours : 10:30


ASEC Report ID : 61335
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 09/06/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. Three thousand seventy-eight (3078) cubic yards of structural-fill materials were placed for 8-inch lift (4) in section 1 area B7 (drawing E720661) and continued the placement of in the section 2 for lift (4) are G7 (drawing E720659) of the basement. The materials were placed in accordance with ITP-001, and the fill area is highlighted in purple on the attached drawing.
2. The basement area was probed using the hand probe and three moisture density tests were performed in the basement followed with a check-plug to verify Proctor curve application. The test locations were marked on the enclosed drawing.
3. French drain installation was observed and documented on this date.
4. Perforated pipe and planned 57 stone was wrapped in the geofabric in the 2 foot wide trench previously excavated.

We appreciate the opportunity to provide our services on this project. Should you have any inquiries or require further discussion about this report, please feel free to contact us. We remain available to address any questions or concerns you may have.

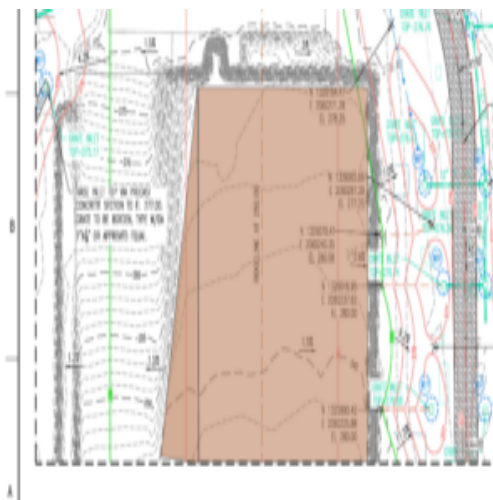

Highlighted region depicts section 1



Highlighted region depicts section 2

Date : 09/06/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/06/2023 6:00
Onsite Hours : 10:30

ASEC Report ID : 61335
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 09/06/2023 16:30
ASEC Technician Name : Avinash Bandham



Lift is placed on section 2



Pipe has been installed in french drain water treatment area



Stone aggregate has been placed on the top of the pipe

Date : 09/06/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/06/2023 6:00
Onsite Hours : 10:30

ASEC Report ID : 61335
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 09/06/2023 16:30
ASEC Technician Name : Avinash Bandham



Geo-fabric has been installed to cover the stone aggregate



Rock Boulders has been placed on the topmost of all the materials



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
