

Date : 09/11/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/11/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61447
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/11/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R5, E720659 S1-R5.)


During the visit, the following observations were made:

1. Three thousand five hundred and sixty-four (3564) cubic yards of structural-fill materials were placed for lift (6) in section 1 basement area B7 (E720661 S1-R8) and for lift (6) in section 2 basement are G7(E720659 S1-R8). The materials were placed and compacted in accordance with ITP-001, and the fill area is highlighted in brown as depicted in the attached drawing.
2. The basement area was probed using the hand probe and three moisture density test were performed in the basement followed with a check-plug. The test locations were marked on the enclosed drawing.
3. Around the HDPE pipe, which functions as a dewatering well located at the southeast corner, aggregate was carefully placed. This serves to facilitate dewatering operations. Subsequently, the aggregate was wrapped with geo-fabric to prevent the migration of fines. This step aligns with the measures specified in ITP-003, aimed at maintaining the integrity of the dewatering system.

We appreciate the opportunity to provide our services on this project. Should you have any inquiries or require further discussion about this report, please feel free to contact us. We remain available to address any questions or concerns you may have.



The highlighted region depicts the placement of structural fill-material in section 2

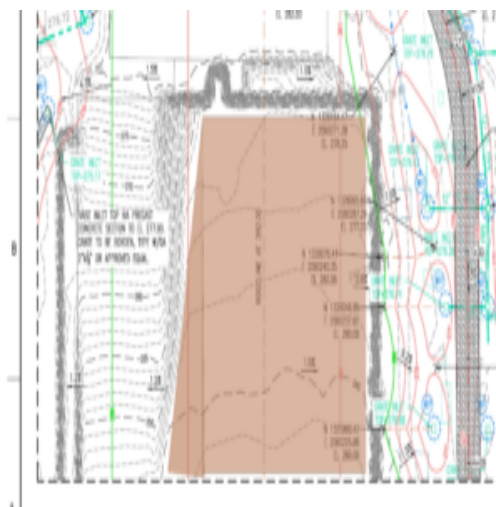

The highlighted region depicts the placement of structural fill-material in section 2

Date : 09/11/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/11/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61447
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/11/2023 16:30
ASEC Technician Name : Avinash Bandham



Date : 09/11/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/11/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61447
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/11/2023 16:30
ASEC Technician Name : Avinash Bandham



Placement of structural fill material in section 2
basement area



Placement of structural fill material in section 2
basement area



Placement of structural fill material in section 2
basement area

Date : 09/11/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/11/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61447
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/11/2023 16:30
ASEC Technician Name : Avinash Bandham



Placement of structural fill material in section 2 basement area



Placed the stone-aggregate around the pipe



Placed the stone-aggregate around the pipe



Placed the stone-aggregate around the pipe

Date : 09/11/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/11/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61447
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/11/2023 16:30
ASEC Technician Name : Avinash Bandham



Placement of structural fill material in section 1



Placement of structural fill material in section 1



Placement of structural fill material in section 1



Covered HDPE pipe with Geo-fabric

Date : 09/11/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/11/2023 06:00
Onsite Hours : 10:30

ASEC Report ID : 61447
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : SUNNY
Departure Time : 09/11/2023 16:30
ASEC Technician Name : Avinash Bandham



Covered HDPE pipe with Geo-fabric



Covered HDPE pipe with Geo-fabric



Covered HDPE pipe with Geo-fabric



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
