

Date : 09/19/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/19/2023 6:00
Onsite Hours : 10:30


ASEC Report ID : 61744
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 09/19/2023 16:30
ASEC Technician Name : Avinash Bandham

AS ENGINEERING AND CONSULTING, LLC (ASEC) representative Avinash Bandam visited the site at the request of Jackson Demolition representative Josh Kelly. The undersigned representative was present to monitor, verify and document the ongoing project activities. (reference drawing E720661 S1 - R5, E720659 S1-R5.)

During the visit, the following observations were made:

1. Two thousand four hundred thirty (2430) cubic yards of structural-fill materials were placed for 8-inch lift (9) in section 1 area B7 (drawing E720661) and continued the placement of in the section 2 for lift (13) are G7 (drawing E720659) of the basement. The materials were placed in general accordance with ITP-001, and the fill area is highlighted in purple on the attached drawing.
2. The basement area was probed using the hand probe and four moisture density tests were performed in the basement followed with a check-plug to verify Proctor curve application. The test locations were marked on the enclosed drawing.

We appreciate the opportunity to provide our services on this project. Should you have any inquiries or require further discussion about this report, please feel free to contact us. We remain available to address any questions or concerns you may have.

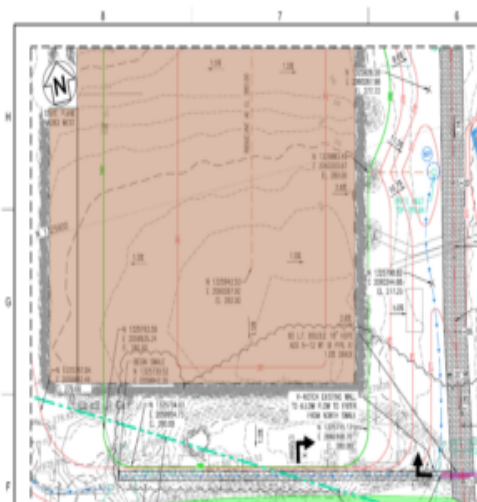

Highlighted region depicts section 2



Lift is placed on section 2

Date : 09/19/2023
Project No : 2022C235
Client Company : Jackson Demolition Service, Inc.
Arrival Time : 09/19/2023 6:00
Onsite Hours : 10:30

ASEC Report ID : 61744
Name of the Project : Plant Gorgas Demolition and Grading
Project Location : 460 Gorgas Rd, Parrish, AL 35580
Weather : Sunny
Departure Time : 09/19/2023 16:30
ASEC Technician Name : Avinash Bandham



Structural fill materials placed on section 2



Hauling is performed in section 2



Ramchandra Mogulla, PE
31220
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
