

Date : 07/26/2023
Project No : 2023C144
Client Company : CCG
Arrival Time : 07/26/2023 08:30
Onsite Hours : 9:30

ASEC Report ID : 60526
Name of the Project : Carodel Farms @ Union Church Rd
Project Location : Flowery Branch
Weather : Cloudy
Departure Time : 07/26/2023 18:00
ASEC Technician Name : Vidal Shengan


Our AS Engineering and Consulting (ASEC) representative visited the Carodel Farms site to conduct quality control inspection and testing services. Visual observation techniques were employed to ensure compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were made on-site:

1. Installation of manhole: contractor installed manhole CB 38 and manhole A-9. The quality control representative visually inspected the installation and verified that it met the project requirements for installation. A placement of the 4 inches of stone at the bottom subgrade was observed.
2. Installation of HDPE Pipe: Between manhole 37 and 38, A-9 and A-10 contractor installed HDPE (High-Density Polyethylene) pipe. Before placing the pipes, the contractor prepared the bottom with 4 inches of stone and also covered the pipes with a 4-inch stone layer. The quality control representative visually assessed the installation and confirmed that it was executed according to the project specifications. Sheet no: c11.1
3. Backfilling Operations: Contractor backfilled soils in Detention Pond 1C. The quality control representative visually inspected the backfilling operations and confirmed that they were performed in accordance with project requirements. Drilling and blasting of Rock: The driller continued rock blasting in the areas where drilling had been performed on Monday and Tuesday. The quality control representative observed the blasting operations and noted that they were carried out safely and in compliance with applicable safety protocols. No incidents or concerns were observed during the blasting process.



Date : 07/26/2023
Project No : 2023C144
Client Company : CCG
Arrival Time : 07/26/2023 08:30
Onsite Hours : 9:30

ASEC Report ID : 60526
Name of the Project : Carodel Farms @ Union Church Rd
Project Location : Flowery Branch
Weather : Cloudy
Departure Time : 07/26/2023 18:00
ASEC Technician Name : Vidal Shengan

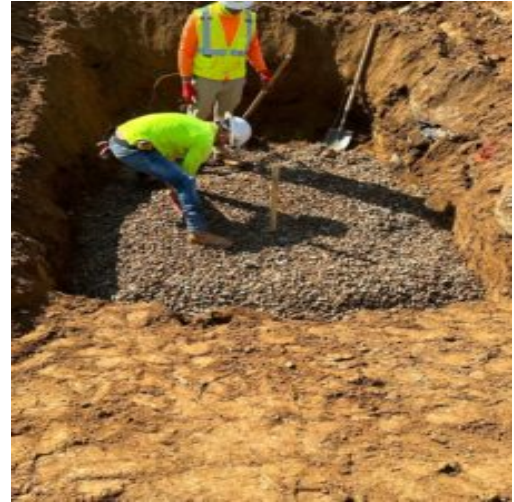

Date : 07/26/2023
Project No : 2023C144
Client Company : CCG
Arrival Time : 07/26/2023 08:30
Onsite Hours : 9:30

ASEC Report ID : 60526
Name of the Project : Carodel Farms @ Union Church Rd
Project Location : Flowery Branch
Weather : Cloudy
Departure Time : 07/26/2023 18:00
ASEC Technician Name : Vidal Shengan



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
