


Date : 08/01/2023
Project No : 2023C144
Client Company : CCG
Arrival Time : 08/01/2023 08:30
Onsite Hours : 08:30

ASEC Report ID : 60724
Name of the Project : Carodel Farms @ Union Church Rd
Project Location : Flowery Branch
Weather : Cloudy
Departure Time : 08/01/2023 17:00
ASEC Technician Name : Vidal Shengan

On 08-01-2023, the AS Engineering and Consulting (ASEC) representative visited the Carodel Farms site to conduct quality control inspection and testing services. Visual observation techniques were employed to ensure compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were made on-site:

1. Installation of Manhole A-9: The contractor installed Manhole A-9 with 4" stone (057) at the bottom before placing the manhole. The quality control representative visually inspected the installation and noted that it met the project requirements.
2. Installation of HDPE Pipe: Between Manhole A-8 and Manhole A-9, the contractor installed HDPE (High-Density Polyethylene) pipe. Before placing the pipes, the contractor prepared the bottom with 4" stone and also covered the pipes with 4" stone. The quality control representative visually assessed the installation and confirmed that it was performed according to the project specifications.
3. Drilling Operations: We recommended to the contractor to do excavate a few pit tests on Lots 60 through 68 near the road to determine the exact mass of rocks in this area so as not to let the driller do unnecessary work and save time. No appreciable rock was encountered in these areas. Contractor then began to lay pipe within the street.

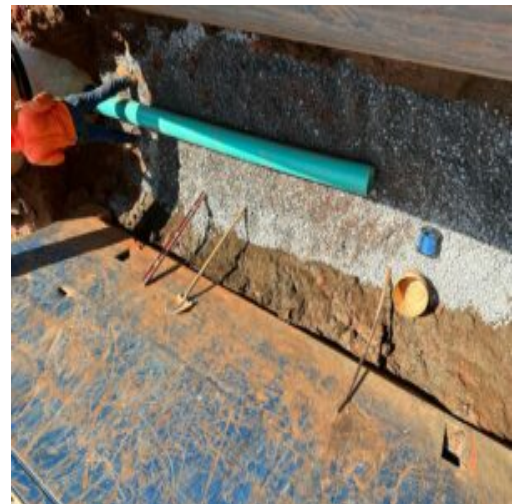

Date : 08/01/2023
Project No : 2023C144
Client Company : CCG
Arrival Time : 08/01/2023 08:30
Onsite Hours : 08:30

ASEC Report ID : 60724
Name of the Project : Carodel Farms @ Union Church Rd
Project Location : Flowery Branch
Weather : Cloudy
Departure Time : 08/01/2023 17:00
ASEC Technician Name : Vidal Shengan



Date : 08/01/2023
Project No : 2023C144
Client Company : CCG
Arrival Time : 08/01/2023 08:30
Onsite Hours : 08:30

ASEC Report ID : 60724
Name of the Project : Carodel Farms @ Union Church Rd
Project Location : Flowery Branch
Weather : Cloudy
Departure Time : 08/01/2023 17:00
ASEC Technician Name : Vidal Shengan



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
