

Date : 04/24/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/24/2026
Onsite Hours : N/A

ASEC Report ID : 93693
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAlA, Atlanta, GA
Weather : overcast
Departure Time : 04/24/2026
ASEC Technician Name : Russell Hendrix

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day:

Area 1

Asphalt paving was performed for one lane. Quality control (QC) was performed by GeoHydro.

Area 2

An unplanned concrete pour was completed for a slab. Refer to the associated photos and testing report for documentation and results.

Area 3

A waterproofing membrane was installed, followed by placement of approximately 6 inches No. 89 stone and corrugated pipe. Backfilling operations commenced. Refer to the testing report for compaction results.

Area 4

Backfilling and placement of soil for the second lift.

Area 6

Sheet piles were cut to below grade (see photos). Corrugated pipe installation was observed with approximately 6 inches of No. 89 stone bedding. Backfilling of the first lift commenced.

Runway Area

Concrete cylinder samples from the previous day's pour around light cans were transported to the CW Matthews laboratory for testing.

Date : 04/24/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/24/2026
Onsite Hours : N/A

ASEC Report ID : 93693
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAlA, Atlanta, GA
Weather : overcast
Departure Time : 04/24/2026
ASEC Technician Name : Russell Hendrix



Backfilling



Asphalt paving Area 1



Testing



Backfilling Area 4

Date : 04/24/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/24/2026
Onsite Hours : N/A


ASEC Report ID : 93693
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAlA, Atlanta, GA
Weather : overcast
Departure Time : 04/24/2026
ASEC Technician Name : Russell Hendrix



Sheet piles cut below grade



Concrete Pour

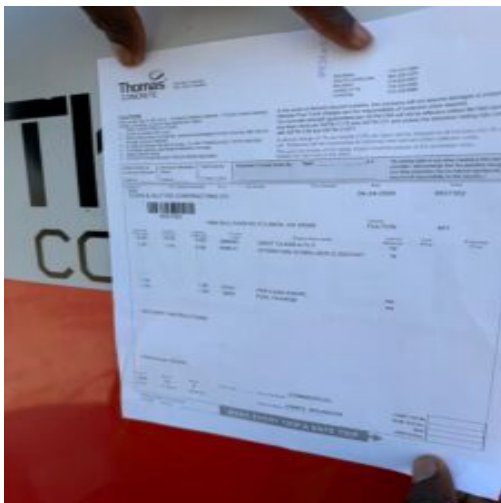

Concrete ticket



New concrete area

Date : 04/24/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/24/2026
Onsite Hours : N/A


ASEC Report ID : 93693
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAlA, Atlanta, GA
Weather : overcast
Departure Time : 04/24/2026
ASEC Technician Name : Russell Hendrix



Sheet Piles being cut down



Sheet piles

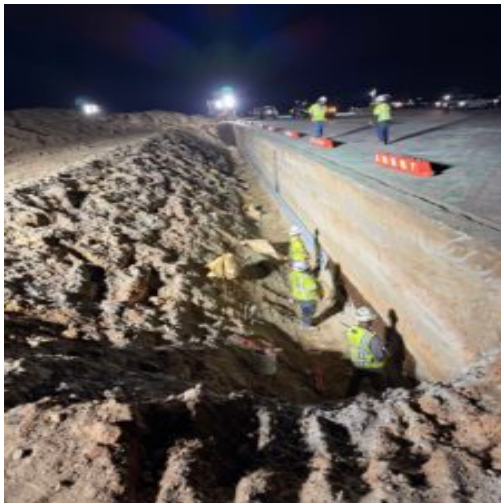

Waterproof membrane being installed

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
