

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026 19:30
Onsite Hours : 10:30

ASEC Report ID : 93628
Name of the Project : Airfield Repairs 2021-23
Project Location : HJIA, Atlanta, GA
Weather : clear
Departure Time : 04/26/2026 06:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Area 2:

Topsoil was placed and evenly spread across the area using a Caterpillar 275 track loader. The material was distributed to achieve uniform coverage in preparation for final grading and surface finishing activities.

Area 4:





Work continued with placement of fill material in controlled lifts of approximately 6-8 inches. Each lift was compacted using a sheep foot roller to ensure proper density and stability. Density tests were performed on alternative lifts, and results met the required compaction. The operation progressed systematically lift by lift following standard compaction procedures.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026 19:30
Onsite Hours : 10:30

ASEC Report ID : 93628
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAlA, Atlanta, GA
Weather : clear
Departure Time : 04/26/2026 06:00
ASEC Technician Name : Samara Simha Reddy Kandi

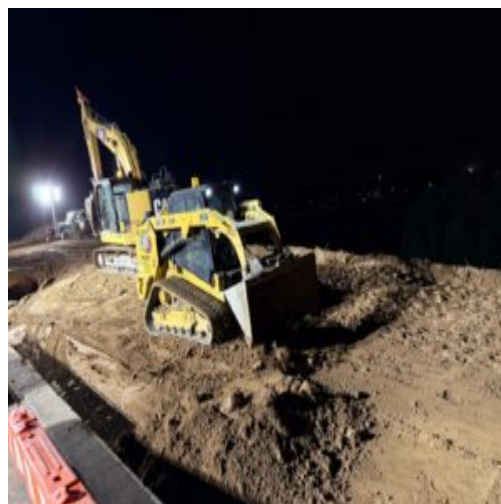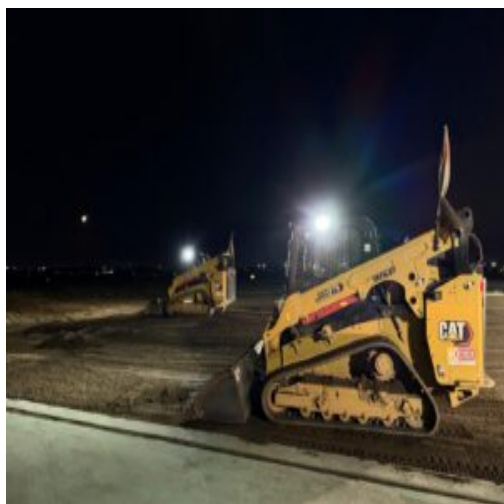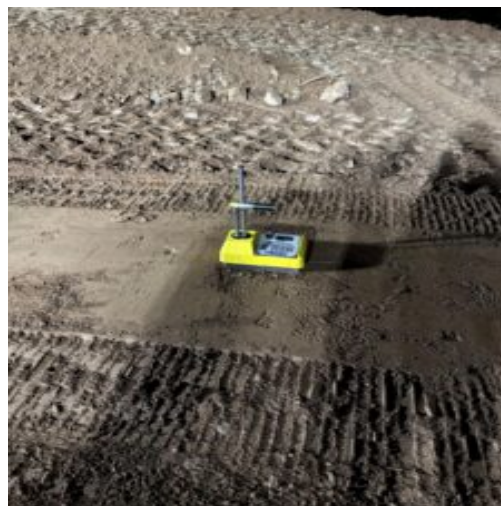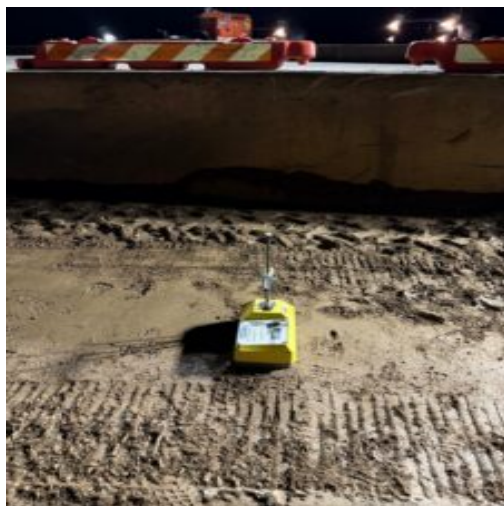

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
