

Date : 11/29/2023
Project No : 2023C195
Client Company : Toll Bros. Inc.
Arrival Time : 11/29/2023 12:00
Onsite Hours : 04:00

ASEC Report ID : 63164
Name of the Project : Kimbal Bridge Tract
Project Location : Alpharetta
Weather : Sunny
Departure Time : 11/29/2023 16:00
ASEC Technician Name : Vidal Dias

On 11/29/2023, the undersigned ASEC representative visited the site to observe the ongoing placement of the sewer line along Road 'C'. This visit was part of our continued effort to observe and document the progress infrastructure installations as per project requirements.

Sewer Line Installation Observations:

- The focus of the visit was the sewer line installation process along Road 'C'. The operation was observed for its adherence to project plans and specifications.
- Piping appeared to be installed in accordance with the project drawings.
- Backfilling operations were also observed. The trench was backfilled in six to eight-inch lifts and compacted.

Compaction and Testing:


- Compaction tests were performed on the compacted backfill material.
- A probe rod was used in conjunction with density testing equipment to verify stability of surficial soils. The probe rod did not exceed two inches in deflection.

Test No.	Dry Density (pcf)	Moisture Content (%)	Wet Density (pcf)	Compaction (%)
1	86.4	31.0	113.1	98.4
2	86.6	30.9	113.4	98.6
3	86.9	31.0	113.8	98.9
4	87.1	30.8	114.0	99.2
5	87.3	31.0	114.3	99.4
6	87.5	30.9	114.5	99.6
7	87.6	31.0	114.7	99.8

If you have any questions or require further clarification regarding the content of this report, please do not hesitate to get in touch. We are readily available to address any inquiries you may have.

Date : 11/29/2023
Project No : 2023C195
Client Company : Toll Bros. Inc.
Arrival Time : 11/29/2023 12:00
Onsite Hours : 04:00

ASEC Report ID : 63164
Name of the Project : Kimbal Bridge Tract
Project Location : Alpharetta
Weather : Sunny
Departure Time : 11/29/2023 16:00
ASEC Technician Name : Vidal Dias

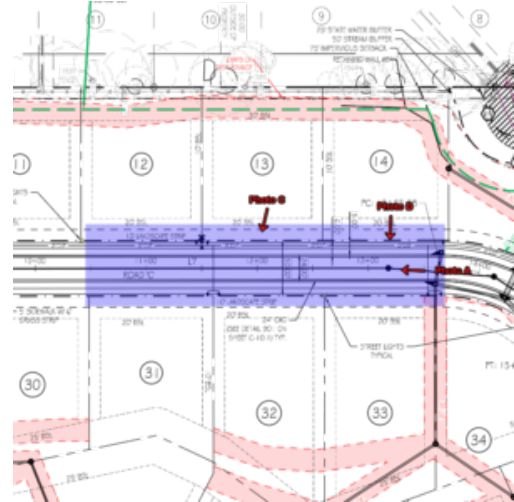

Vidal Dias

Vidal Dias

-
Project Geologist

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
