

Date : 01/02/2024  
Project No : 2023C201  
Client Company : Artisan Built Communities  
Arrival Time : 01/02/2024 08:00  
Onsite Hours : 06:00

ASEC Report ID : 63564  
Name of the Project : Jasons Walk - Era Drive  
Project Location : Era Drive, Cumming, GA  
Weather : sunny  
Departure Time : 01/02/2024 14:00  
ASEC Technician Name : Vidal Dias

The undersigned ASEC representative was on site as requested by the Client and/or Contractor to observe contractor's field activities. Visual observation techniques were employed to evaluate work in-place for general compliance with the Project Plans, Specifications, Codes and Standards, and Material Submittals.

## Overview and Observations


During the site visit on January 2, 2024, key activities included conducting a moisture content test and observing site preparation activities. The in-place moisture content was found to be 30.2%, which is above the optimum level of 20.6%. Consequently, soil placement activities were suspended. Instead, the contractor focused on preparing the green space behind Lots #20-25, as marked in red on the attached drawing. Scarification and aeration of the high moisture soils should be performed prior to their use as fill.

## Moisture Test Results

- **Test Conducted:** On-site moisture content measurement.
- **Results:** Moisture content recorded at 30.2%, exceeding the optimum of 20.6%.

## Site Preparation Activities

- **Location:** Green space behind lots 20-25.
- **Activity Observed:** Site preparation in response to current soil conditions.

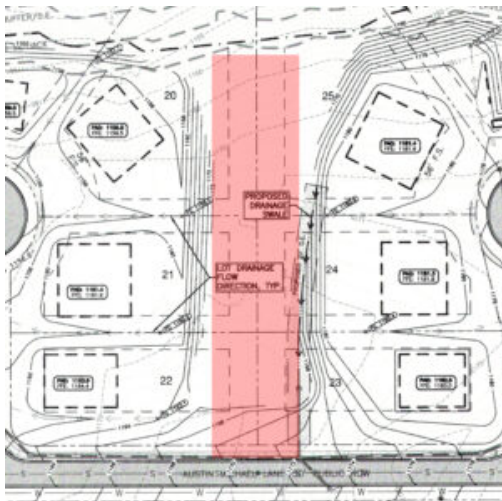

Date : 01/02/2024  
Project No : 2023C201  
Client Company : Artisan Built Communities  
Arrival Time : 01/02/2024 08:00  
Onsite Hours : 06:00

ASEC Report ID : 63564  
Name of the Project : Jasons Walk - Era Drive  
Project Location : Era Drive, Cumming, GA  
Weather : sunny  
Departure Time : 01/02/2024 14:00  
ASEC Technician Name : Vidal Dias



Vidal Dias

-  
**Project Geologist**

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
