

Date : 05/03/2024
Project No : 2024C112
Client Company : SR Homes
Arrival Time : 05/03/2024 9:00
Onsite Hours : 9:00

ASEC Report ID : 66341
Name of the Project : Sterlington
Project Location : Canton
Weather : sunny
Departure Time : 05/03/2024 18:00
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The undersigned arrived onsite to observed CMU block retaining wall #1 placement.

The undersigned noted the base course was placed behind the block and in the cells with #57 stone.

Every 3rd course of block, a geotextile reinforcement was placed (Geo-grid). Soil backfill was placed in 12-inch lifts and compacted using 12 ton pad-foot and trench compactor.

No. 57 stone was utilized 1 foot behind the block and within the cells.


A drainage pipe outlet (weep hole) was installed every 50 feet.

In case of any questions or concerns with regards to our observations or recommendations stated in this report we will be more than glad to discuss them with you.



Date : 05/03/2024
Project No : 2024C112
Client Company : SR Homes
Arrival Time : 05/03/2024 9:00
Onsite Hours : 9:00

ASEC Report ID : 66341
Name of the Project : Sterlington
Project Location : Canton
Weather : sunny
Departure Time : 05/03/2024 18:00
ASEC Technician Name : Aminullah Azimi

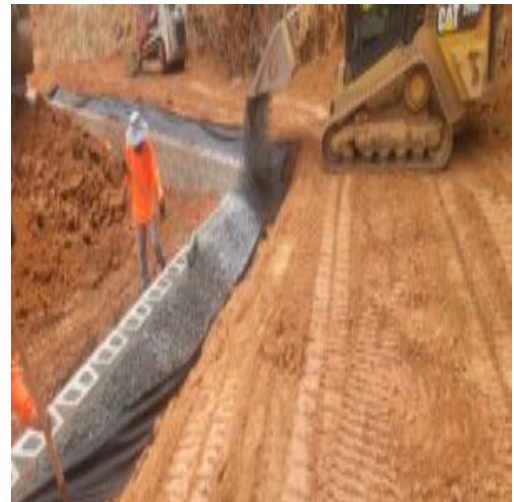

Date : 05/03/2024
Project No : 2024C112
Client Company : SR Homes
Arrival Time : 05/03/2024 9:00
Onsite Hours : 9:00

ASEC Report ID : 66341
Name of the Project : Sterlington
Project Location : Canton
Weather : sunny
Departure Time : 05/03/2024 18:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
