




Date : 06/28/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 06/28/2024 08:30
Onsite Hours : 08:30

ASEC Report ID : 67385
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Cloudy
Departure Time : 06/28/2024 17:00
ASEC Technician Name : Fawad Shagiwal

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services.

The following observations were observed on the site this day:

- The placement and compaction of backfill for Lots #66 to 73 and #80 to 88 progressed using CP54B, RA30, D51PX and CAT330 compaction equipment.
- The new trench was dig, excavated and built at the inlet area of the existing detention pond for the installation and placement of storm water manholes and sewer line.
- Installation and placement of ST M-2 4'0/5 and ST N-2 4'0/5 storm water manholes and storm lines were in progress.
- At the time of arrival our representative observed that work was in progress for Lots #66-73 and #80-88 with 2-foot lifts being placed and compacted using CP54B and D51PX equipment.

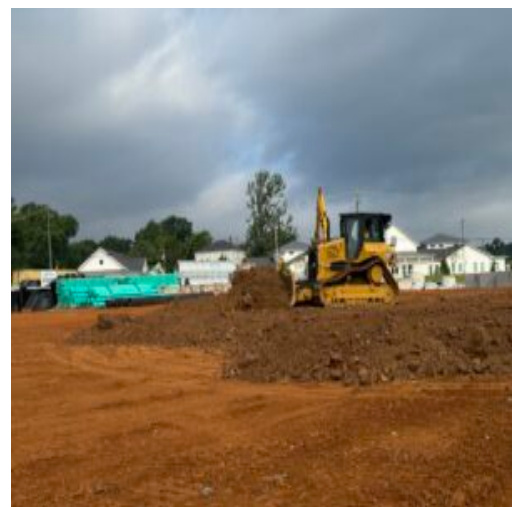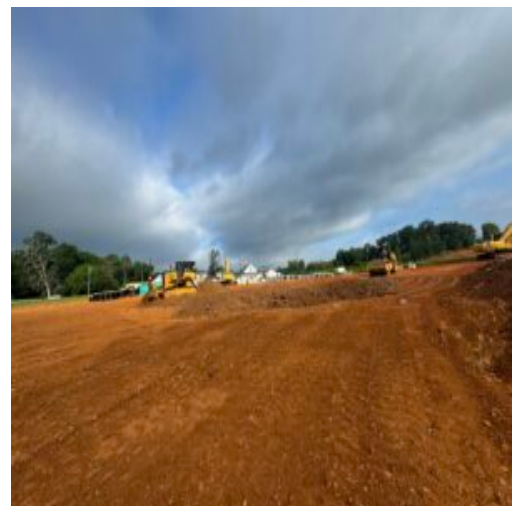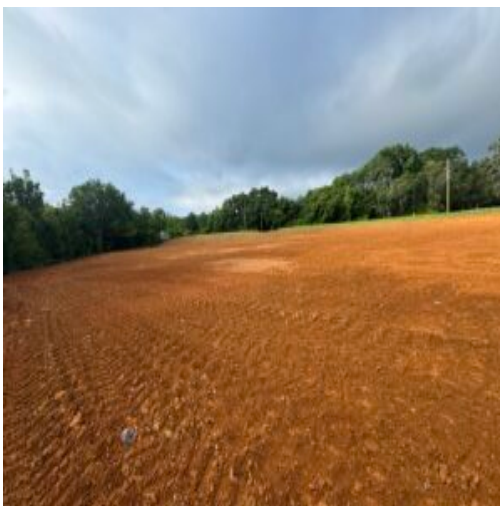

Date : 06/28/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 06/28/2024 08:30
Onsite Hours : 08:30

ASEC Report ID : 67385
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Cloudy
Departure Time : 06/28/2024 17:00
ASEC Technician Name : Fawad Shagiwal



Date : 06/28/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 06/28/2024 08:30
Onsite Hours : 08:30

ASEC Report ID : 67385
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Cloudy
Departure Time : 06/28/2024 17:00
ASEC Technician Name : Fawad Shagiwal



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
