


Date : 09/03/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 09/03/2024 08:30
Onsite Hours : 08:30

ASEC Report ID : 69413
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Sunny
Departure Time : 09/03/2024 17:00
ASEC Technician Name : Fawad Shagiwal

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawings/specifications, applicable codes and material submittals.

The following observations were observed on the site this day.

- The placement and compaction of backfill soil for Lots #89 to 97 progressed with one (1) foot lifts being placed and compacted using sheeps-foot (CP54B), (RA30), (D61PX) and (CAT330) equipment.
- Excavation and preparation of trenches for placement and installation of storm water lines, manholes and sewer lines and manholes progressed.
- Installation and placement of sewer lines and manhole SSA3 continued.
- Installation and placement of storm water line from manhole CIA11 to CIA12 continued.
- Installation and placement of storm water manholes CIA11 and CIA12 were completed.
- One (1) foot lifts were placed and compacted for the trench between storm water manholes CIA11 and CIA12 using trench packer (BMP8500) and sheeps-foot (CP54B) equipment.
- Two (2) foot lifts were being placed and compacted for sewer manhole SSA3 using sheeps-foot (SV204T) equipment.
- 15CR GAB placement continued for the entrance road.
- Density test results indicate that the compacted material met the project requirements of 95% the maximum dry density obtained by the (Standard Proctor ASTM 698).

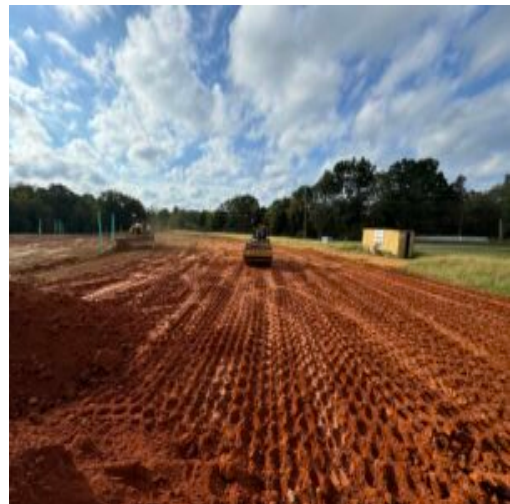

Date : 09/03/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 09/03/2024 08:30
Onsite Hours : 08:30

ASEC Report ID : 69413
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Sunny
Departure Time : 09/03/2024 17:00
ASEC Technician Name : Fawad Shagiwal



Date : 09/03/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 09/03/2024 08:30
Onsite Hours : 08:30

ASEC Report ID : 69413
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Sunny
Departure Time : 09/03/2024 17:00
ASEC Technician Name : Fawad Shagiwal



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
