

Date : 08/01/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 08/01/2024 13:00
Onsite Hours : 05:00

ASEC Report ID : 68416
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : sunny
Departure Time : 08/01/2024 18:00
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


- The placement and compaction of fill for Lots #163, 164, 165, 166, 167, 168, and the sewer trench between MH A-7 to MH A-8 and A-9, continued this day.
- At the time of arrival, our representative observed that work was in progress with 1-foot lifts being placed and compacted using 810F and CP56B compaction equipment. Compaction testing was performed using a Troxler nuclear density gauge, along with general probing using a 3/8" diameter probe rod.
- Density test results indicate that most of the compacted materials met the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698. Contractor was informed of testing results and that recompacting in these areas was required.
- Note: In-situ moisture contents were over 3 percent over optimum moisture contents on several tests.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 08/01/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 08/01/2024 13:00
Onsite Hours : 05:00

ASEC Report ID : 68416
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : sunny
Departure Time : 08/01/2024 18:00
ASEC Technician Name : Aminullah Azimi

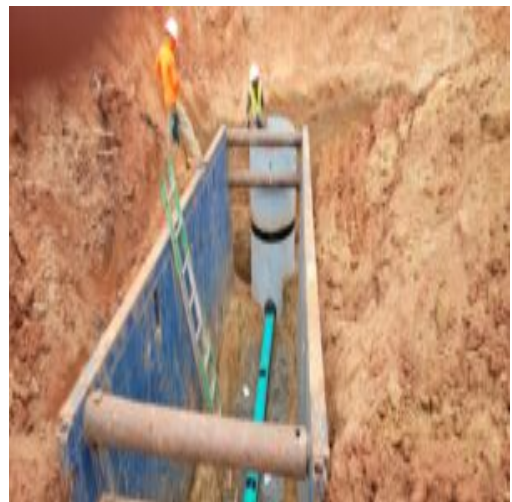

Date : 08/01/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 08/01/2024 13:00
Onsite Hours : 05:00

ASEC Report ID : 68416
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : sunny
Departure Time : 08/01/2024 18:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
