



Date : 09/25/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 09/25/2024 10:00
Onsite Hours : 05:30

ASEC Report ID : 70738
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : cloudy
Departure Time : 09/25/2024 15:30
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

- The placement and compaction of backfill soils for the storm water trench, between MHA2.4.2, MHA2.4.3, MHA2.4.4 continued this day.
- At the time of arrival, our representative observed that work was in progress with 2-foot lifts being placed (see pictures) and compacted using CP56B and trench compaction equipment. Compaction testing was performed using the Standard Test Method for Density of Soil in Place by Drive-Cylinder (ASTM D 2937), along with general probing using a 3/8" diameter probe rod.
- Density test results indicate that most of the compacted materials did not meet the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698. The contractor was informed: (Israel Guerra, 678-749-2198, and Victor 770-733-6729 both of (ALGC) company name)

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

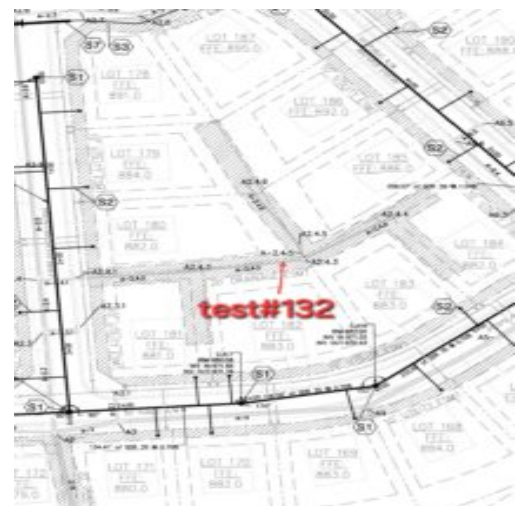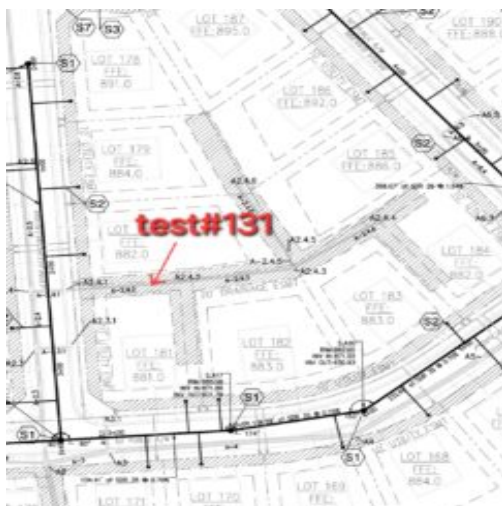

Daily Field Report

Date : 09/25/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 09/25/2024 10:00
Onsite Hours : 05:30

ASEC Report ID : 70738
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : cloudy
Departure Time : 09/25/2024 15:30
ASEC Technician Name : Aminullah Azimi



Date : 09/25/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 09/25/2024 10:00
Onsite Hours : 05:30

ASEC Report ID : 70738
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : cloudy
Departure Time : 09/25/2024 15:30
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
