


Date : 09/30/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 09/30/2024 8:30
Onsite Hours : 08:30

ASEC Report ID : 70827
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : cloudy
Departure Time : 09/30/2024 17:00
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

- The placement and compaction of backfill soils for the sewer trench, between MHSA18 to MHSL1 and storm water trench, MHA2.4.5, MHA2.4.6, MHA2,9 to MHA2.10, continued this day.
- At the time of arrival, our representative observed that work was in progress with 1-foot lifts placed atop of pipes. Due to wet site conditions, the contractor didn't continue backfilling this day.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

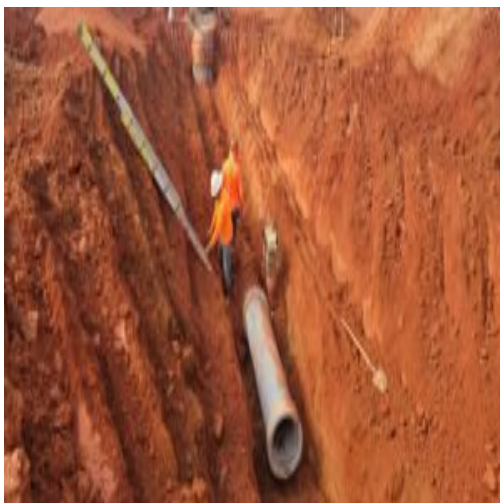

Date : 09/30/2024
Project No : 2024C168
Client Company : CCG
Arrival Time : 09/30/2024 8:30
Onsite Hours : 08:30

ASEC Report ID : 70827
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson
Weather : cloudy
Departure Time : 09/30/2024 17:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
