

Date : 01/02/2025
Project No : 2024C202
Client Company : CCG
Arrival Time : 01/02/2025 07:30
Onsite Hours : 06:00

ASEC Report ID : 74982
Name of the Project : Old Griffin Rd - Hawthorne Reserve
Project Location : Dallas
Weather : Sunny
Departure Time : 01/02/2025 13:30
ASEC Technician Name : Solomon Cherie


Our AS Engineering & Consulting (ASEC) representative arrived on site to observe field activities. The following tasks were performed:

Upon our arrival, our representative observed that the site was still too wet and muddy to continue grading activities. Following a discussion with the grading contractor, the contractor decided to work on soil placement in greenbelt (non-structural) areas. Further sewer line trenching would also continue (no backfilling).

Please contact us if you have any questions regarding this report.



Picture showing green area backfill

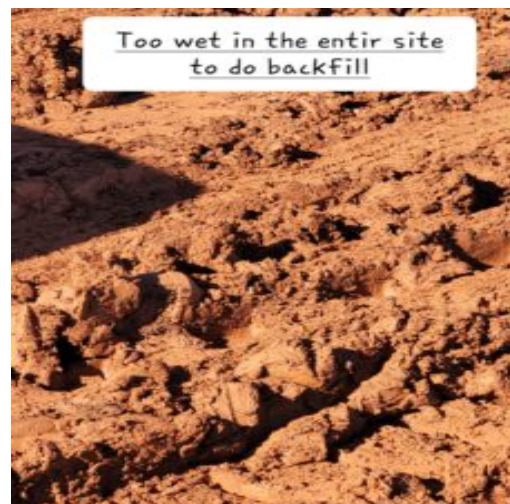

Entire site was wet like the figure above

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
