

Date : 08/22/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 08/15/2024 08:00
Onsite Hours : 9:45

ASEC Report ID : 68819
Name of the Project : Naturewalk at 7 Hills Amenities
Project Location : Dallas
Weather : Cloudy
Departure Time : 08/15/2024 17:45
ASEC Technician Name : Solomon Cherie


Upon arrival the driller was preparing the site and immediately started drilling. During the day I was monitoring each hole while the drilling was done. I was recording the depth where the drilling beat hit bed rock and at what depth was the drilling completed for each hole. Finally, I cross check with the driller.

A attached is my data sheet for the day and the drillers data sheet for the the day and the previous day.

The above-mentioned AS Engineering and Consulting (ASEC) representative, visited the Naturewalk at 7 Hills Amenities site to conduct quality control inspection and testing services. Visual observation techniques were employed to ensure compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were made on-site:

- Rock Volume Determination for the blast was performed on this date: Rock volume was determined based on the attached drill logs. Drilling was performed on the days leading to today and depths to top of rock and termination was recorded.
- Drilled 176 blasting holes and completed 99 blasting locations.
- The total quantity of mass rock shot on this day was calculated to be **2,742.2** cubic yards.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

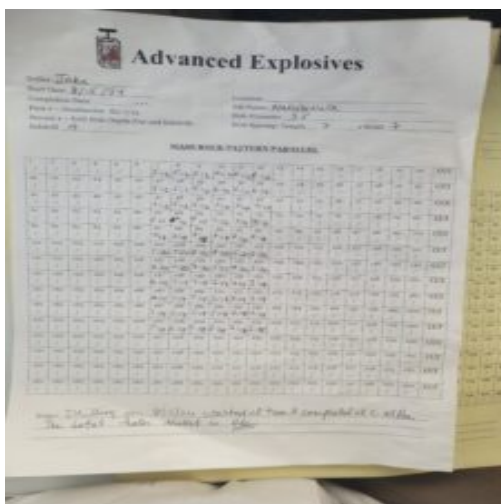

Above is my data sheet.



The drillers data sheet, the previous day data is covered to identify and cross check the two data sheets.

Kenneth Mosman

Kenneth Mosman

Date : 08/22/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 08/15/2024 08:00
Onsite Hours : 9:45

ASEC Report ID : 68819
Name of the Project : Naturewalk at 7 Hills Amenities
Project Location : Dallas
Weather : Cloudy
Departure Time : 08/15/2024 17:45
ASEC Technician Name : Solomon Cherie

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
