

Date : 04/20/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 04/20/2026 8:00
Onsite Hours : -2:00

ASEC Report ID : 93750
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : clear and sunny
Departure Time : 04/20/2026 6:00
ASEC Technician Name : Narayana Ganesh Undavalli

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes and materials submittals. The following observations were observed on site this day.

Crew continued working at the retaining wall. Manhole risers were installed as the fill material reached the required grade at each structure. Fill material was placed in lifts and compacted using a jumping jack and trench compactor in areas around manholes and close to the wall. The remaining areas were compacted using both a caterpillar 815 and a sheep-foot roller.

At wall 5, the crew continued wall construction by placing CMU blocks in accordance with the project plans. Fill material was placed along the wall in lifts and compacted using a trench and sheep-foot roller.


At the Buford neighborhood site, the crew continued trench excavation using a hydraulic excavator equipped with a rock grinder to achieve the required depth.

we appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 04/20/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 04/20/2026 8:00
Onsite Hours : -2:00

ASEC Report ID : 93750
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : clear and sunny
Departure Time : 04/20/2026 6:00
ASEC Technician Name : Narayana Ganesh Undavalli

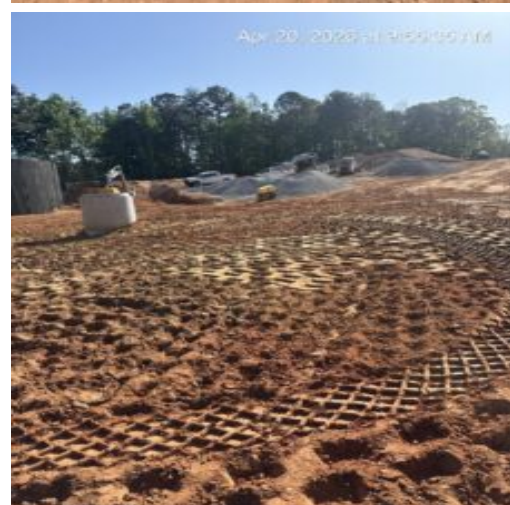

Date : 04/20/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 04/20/2026 8:00
Onsite Hours : -2:00

ASEC Report ID : 93750
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : clear and sunny
Departure Time : 04/20/2026 6:00
ASEC Technician Name : Narayana Ganesh Undavalli



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
