

Date : 05/20/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 05/20/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 94683
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 05/20/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Crew continued working at Wall 4 by installing CMU blocks in accordance with the project plans and specifications. After the block installation, fill material was placed in lifts and each lift was compacted using a trench compactor and sheep-foot roller to achieve density and stability. Additional fill material was also placed behind the wall in a single lift and compacted using a trench compactor.

Another crew continued working in the temporary pond area near CO@R/W, where fill material was placed in lifts, spread evenly with a crawler bulldozer, and compacted using a sheep-foot roller.

A separate crew worked between manhole 2.3CB and manhole 3.1CB, where approximately 25 feet of DIP pipe was installed. The crew prepared and leveled the sub-grade, placed No. 59 stone for bedding, and installed the pipe. Backfill material was then placed in lifts around the pipe and compacted using both a trench compactor and a mini sheep-foot roller.


No activities were performed at the Neighborhood Buford area on this day.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 05/20/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 05/20/2026 08:00
Onsite Hours : 07:00

ASEC Report ID : 94683
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 05/20/2026 15:00
ASEC Technician Name : Samara Simha Reddy Kandi

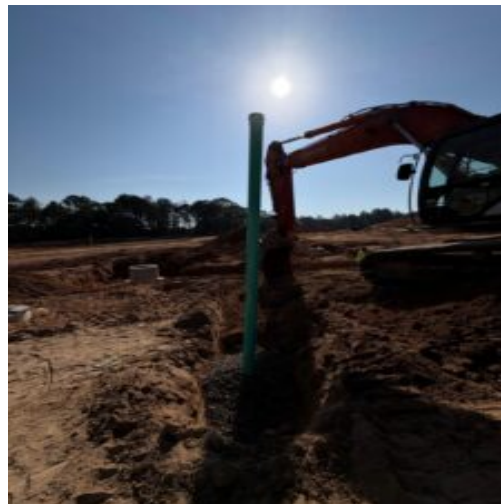

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
