

Date : 05/28/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 05/28/2026 11:
Onsite Hours : NaN:00

ASEC Report ID : 95344
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : clear and sunny
Departure Time : 05/28/2026 5
ASEC Technician Name : Narayana Ganesh Undavalli


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Crew continued working beside retaining wall #1. Fill material was placed in lifts, spread using a crawler bulldozer, and compacted using both a sheep-foot roller and a Caterpillar815. Density tests were performed, and the results met the required project compaction specifications.

At the neighborhood site the crew started excavation and placing storm drainpipe and placed No.57 stone around the drainpipe and fill material was then placed and compacted using a sheep-foot roller.


At the Buford neighborhood site, the crew continued trench excavation using a hydraulic excavator equipped with a rock grinder to achieve the required depth and width.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

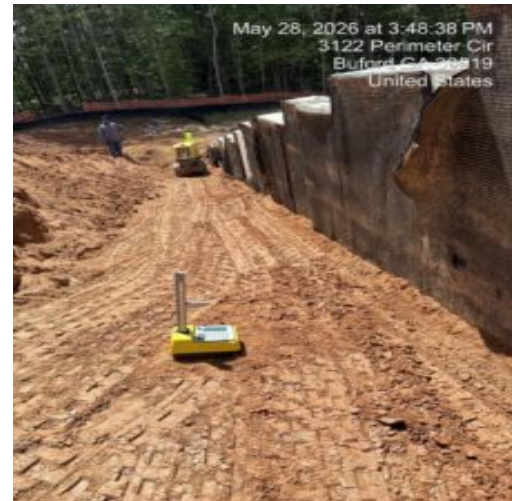

Date : 05/28/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 05/28/2026 11:
Onsite Hours : NaN:00

ASEC Report ID : 95344
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : clear and sunny
Departure Time : 05/28/2026 5
ASEC Technician Name : Narayana Ganesh Undavalli

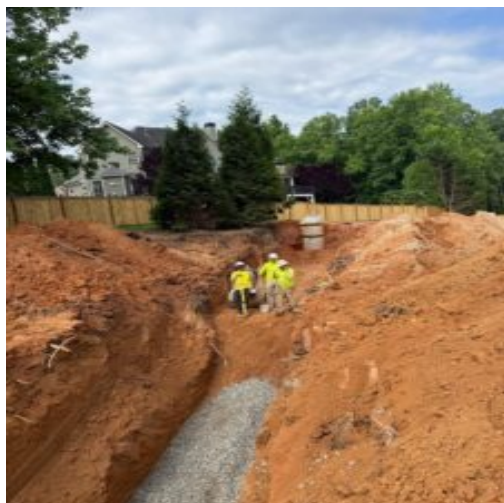

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
