

Date : 09/03/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 09/03/2025 08:30
Onsite Hours : 07:00


ASEC Report ID : 85171
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : Sunny
Departure Time : 09/03/2025 15:30
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested by the contractor (Wilbanks) for the observation/testing of the placement of fill/backfill. The contractor placed lifts of approximately 8-12 inches and compacted via a sheep-foot roller. Fill was placed on Lot #170. The contractor placed topsoil in greenspace areas located along Lots #172 and #173. Our representative density tested the structural fill placed on Lot #170 and provided test results to the contractor.

Our ASEC representative met with the paving crew and county officials to perform a proof-roll of the main entrance and partially of phase 1 roadways. The paving crew and county officials agreed that the proof-roll displayed no signs of significant pumping and/or rutting.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

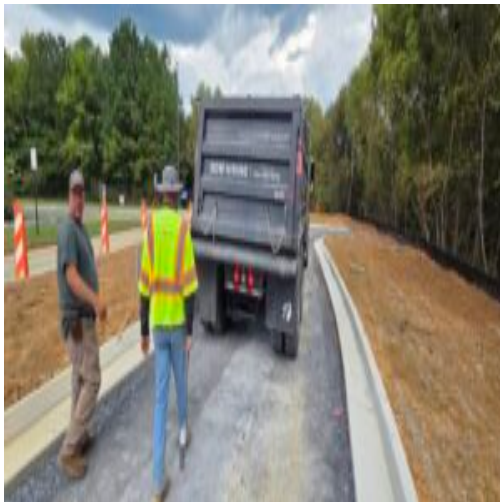

proof roll with pavers and county officials



Date : 09/03/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 09/03/2025 08:30
Onsite Hours : 07:00

ASEC Report ID : 85171
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : Sunny
Departure Time : 09/03/2025 15:30
ASEC Technician Name : Sean Willett



cutting roadways



paving crew

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
