

Date : 12/01/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 12/01/2025 07:30
Onsite Hours : 05:30

ASEC Report ID : 88278
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 12/01/2025 13:00
ASEC Technician Name : Sean Willett


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested by the contractor (NG Grading) for the observation/testing of the placement of fill/backfill. Upon arrival to the site, the surface appeared to be saturated from the rainfall over the previous weekend. The contractor stripped approx. 6 inches to 1 foot off of the Lots #8 through #13 and #52 through #60 area. Then the contractor compacted this area with a sheep-foot roller and began to place fill in approximately 6 to 8-inch lifts. The moisture contents were checked via the dry back method and moisture content was found to be within optimum range. Density testing was performed, and test results were provided to the contractor. ASEC watched as loaded off road trucks rolled across the lifts for an added stability check. There were no signs of pumping or deflection present, and the lifts appear to be stable.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



8 - 13 and 52 - 60 area

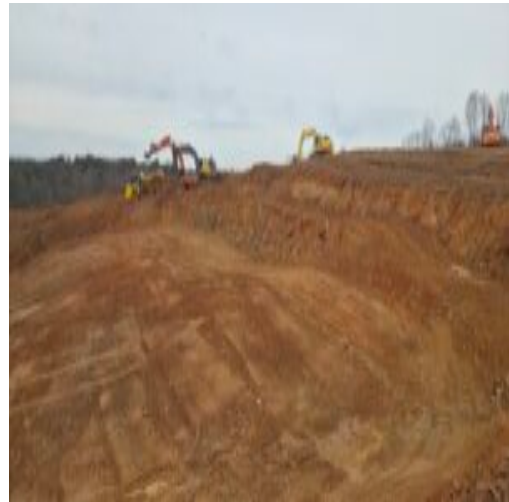

cut from above 8 - 13 and 52 - 60 area

Date : 12/01/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 12/01/2025 07:30
Onsite Hours : 05:30

ASEC Report ID : 88278
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 12/01/2025 13:00
ASEC Technician Name : Sean Willett



commercial lot area



commercial lot area



front detention pond



8 - 13 and 52 - 60 area

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
